




City of West Hollywood
California 1984

WEHO | DESIGN DISTRICT STREETSCAPE

Construction Updates
February 16, 2023



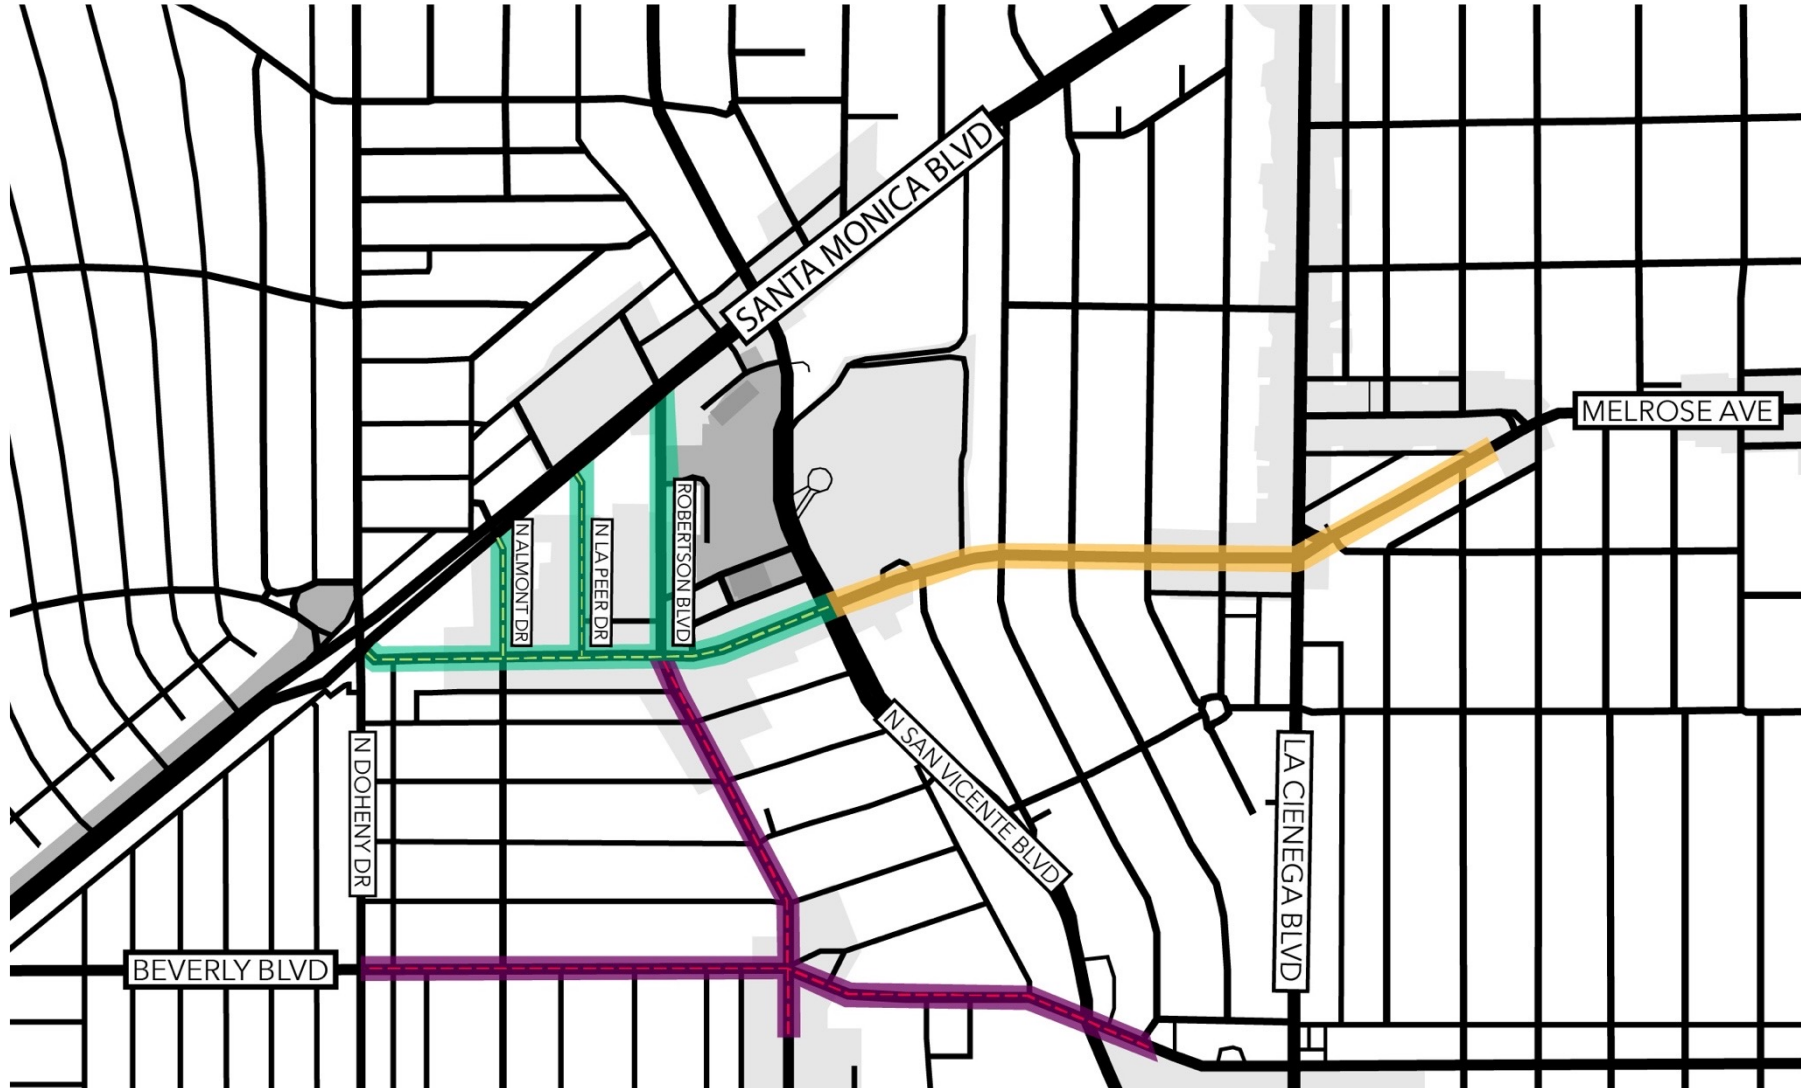

IMPROVEMENT PHASES

Streetscape Phases

- Phase 2 (5/22 – 12/23)
- Phase 3 (2025)
- Phase 5 (2026)

Underground Phases


- Phase 1A
Undergrounding
(Melrose) (4/22 – 5/23)
- Phase 1B
Undergrounding
(Almont + La Peer) (23 – 24)
- Phase 4
Undergrounding (2025)



Melrose Ave & N San Vicente Blvd

Phase 1A

*Utility Undergrounding on
Melrose Avenue*

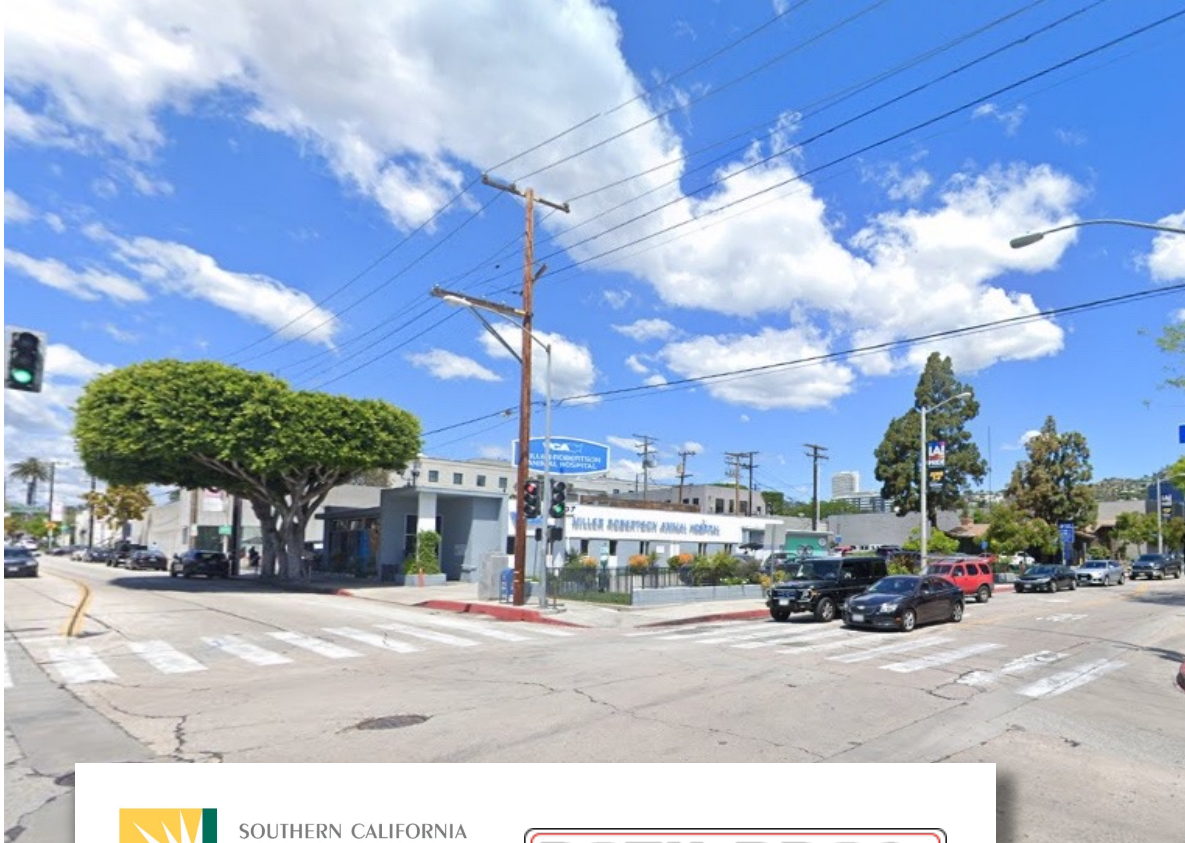

Utility Undergrounding

Southern California Edison (SCE) is leading the utility undergrounding phase in cooperation with the City of West Hollywood and Berg.



Phase 2

Streetscape on
Melrose Avenue

An aerial photograph of a city street intersection. A large orange diagonal band runs from the bottom-left towards the top-right. The band is divided into two sections: the upper section is labeled 'NORTH SIDE' and the lower section is labeled 'SOUTH SIDE'. A green oval is located in the upper right portion of the orange band. The street is labeled 'LA CIENEGA BLVD' on the left and 'CROFT AVE' on the right. The surrounding area includes various buildings, parking lots, and trees.

LA CIENEGA BLVD

NORTH SIDE
SOUTH SIDE

CROFT AVE

Start: October 6, 2022

South Side: Approx. 3.5 months

North Side: Approx. 3 months

Working Hours: 8AM – 5PM

Monday – Friday


Construction Activities:

- Sidewalk removal
- Removed and replaced curb & gutter
- Completed asphalt slot paving (between gutter and roadway)
- Utility work
- Excavating and installing silva cells

Upcoming Work:

- Construct sidewalks
- Install irrigation in planters
- Complete traffic signal work



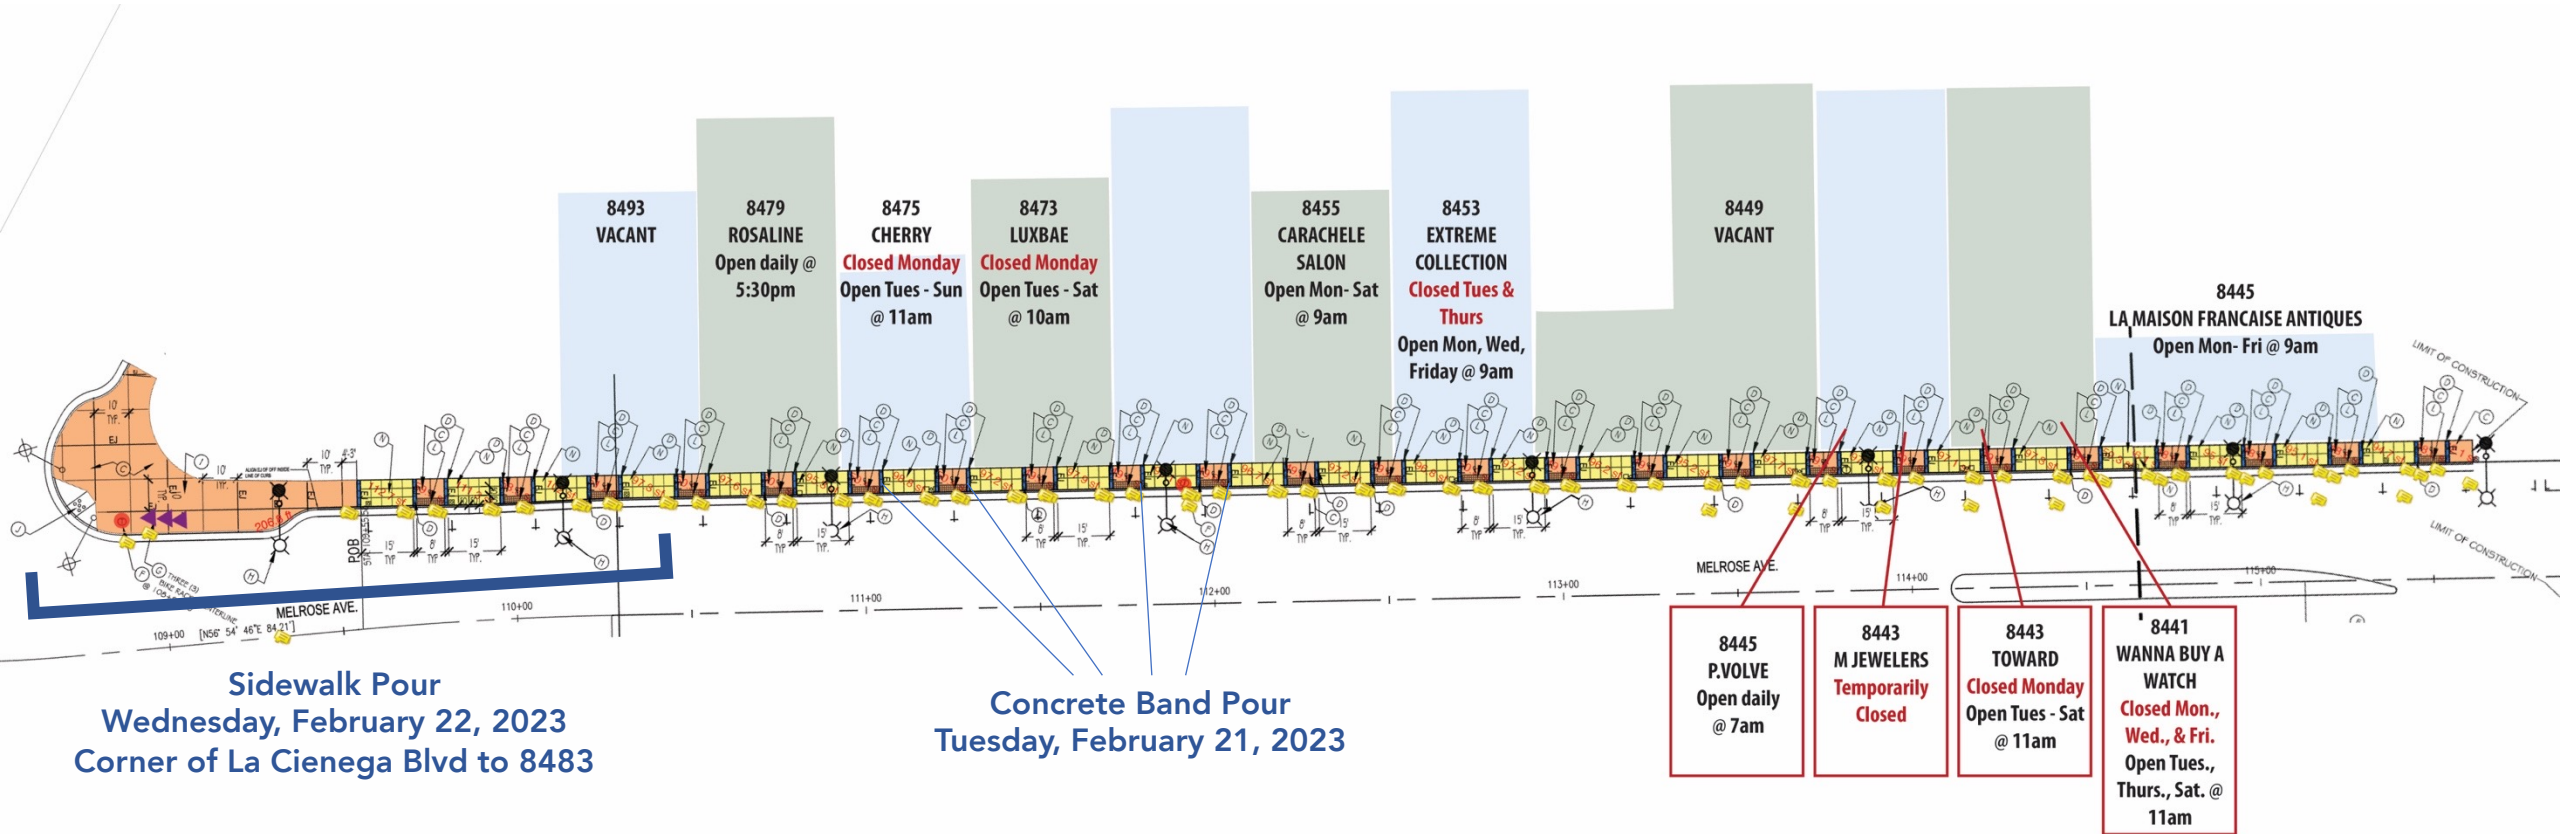

February 15 – 21, 2023

Excluding weekends

9AM – 4PM

Spectrum/Charter Communications

- No parking where posted




February 21 - 23, 2023

9AM – 4PM

Spectrum/Charter Communications

- No parking where posted
- Driveway access will be maintained
- Flaggers to direct vehicles and pedestrians

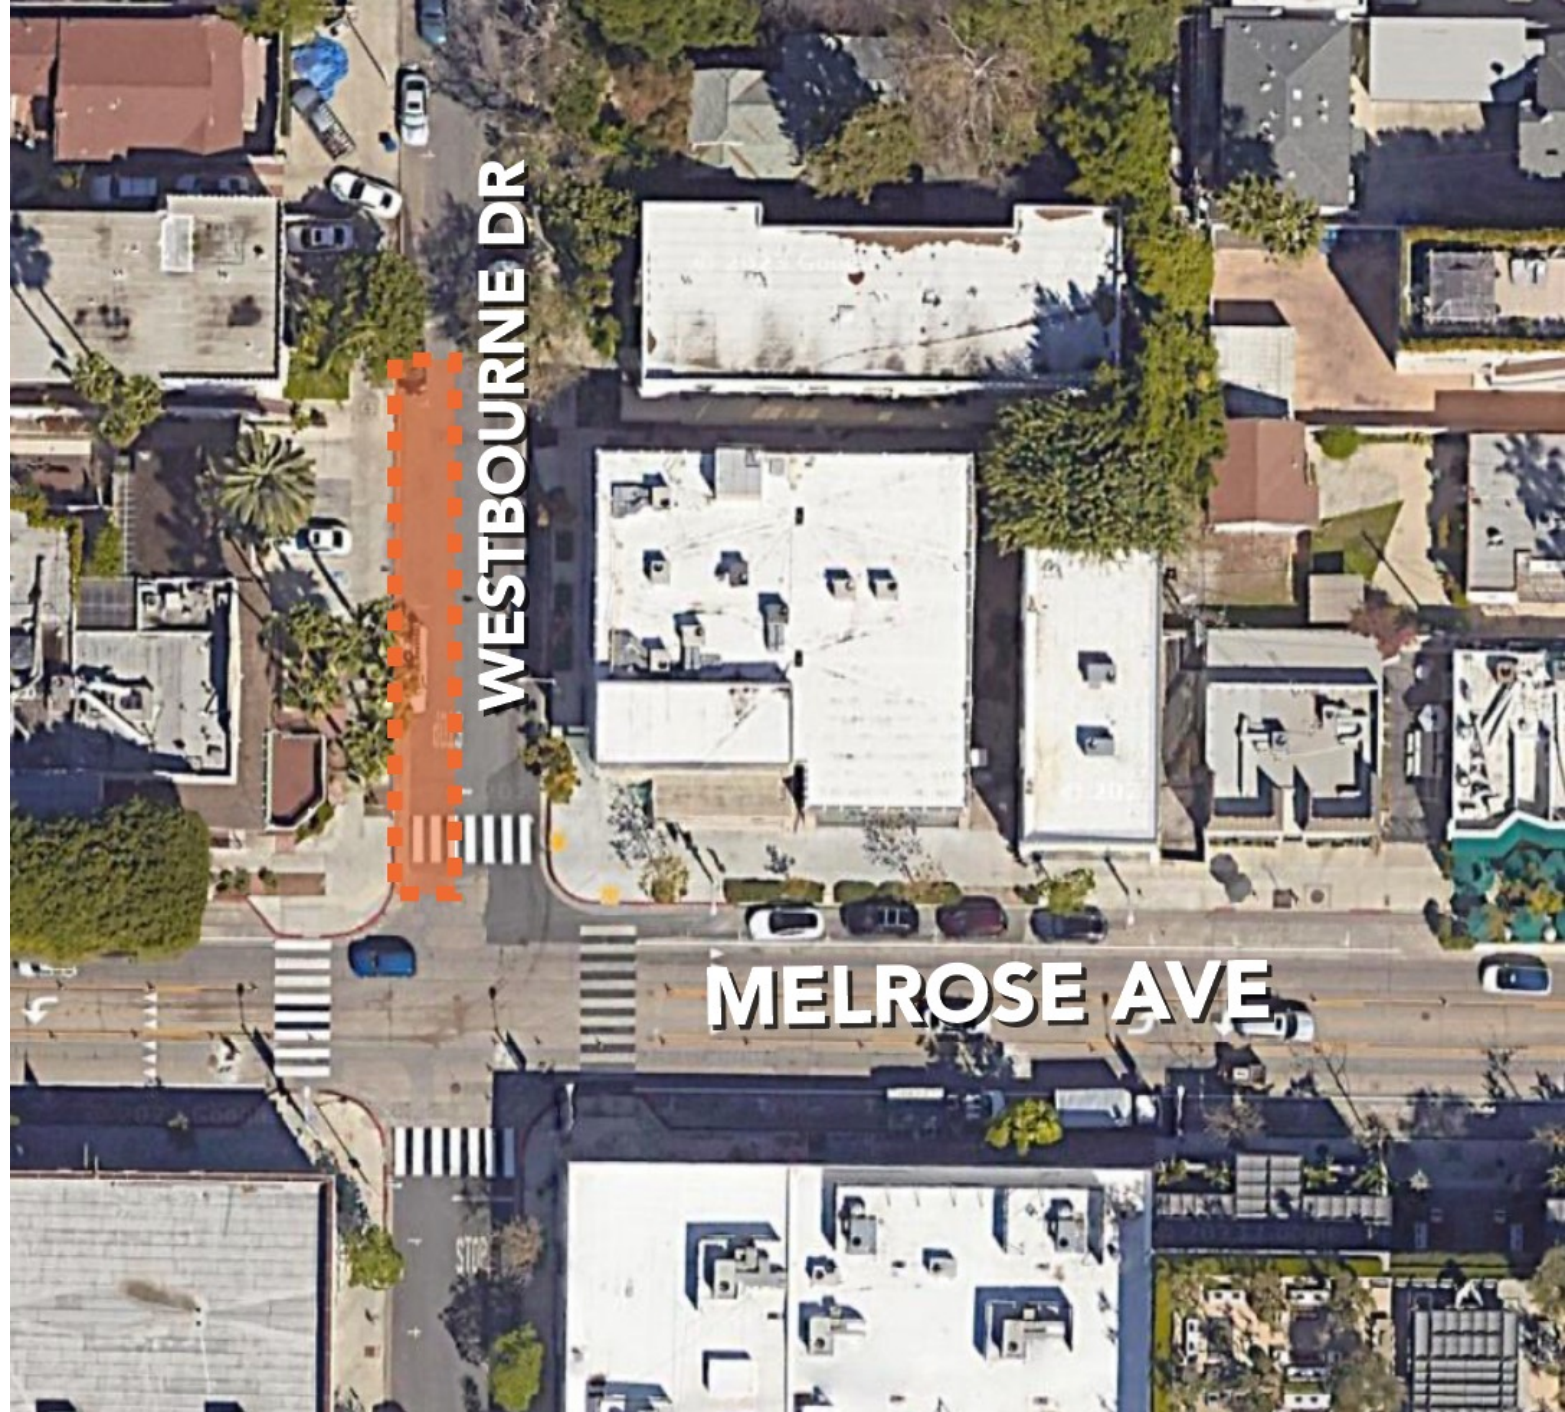

February 21 - 27, 2023

Excluding weekends
8AM – 5PM

SoCal Gas Company

- No parking where posted
- Eastbound traffic on Melrose:
 - One through lane
 - One dedicated left turn lane
 - Right turn permitted



March 1 – 6, 2023

Excluding weekends
9AM – 4PM

Spectrum/Charter Communications

- No parking where posted
- Driveway access will be maintained



Private Developer Work La Peer Dr Storm Drain

Approx. Feb 21 – end of May



Tentative Schedule – Weather Pending

February 2023

January '23							March '23						
S	M	T	W	T	F	S	S	M	T	W	T	F	S
1	2	3	4	5	6	7				1	2	3	4
8	9	10	11	12	13	14	5	6	7	8	9	10	11
15	16	17	18	19	20	21	12	13	14	15	16	17	18
22	23	24	25	26	27	28	19	20	21	22	23	24	25
29	30	31					26	27	28	29	30	31	

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
12	13	14	15 Spectrum Melrose @ Robertson	16 Spectrum Melrose @ Robertson	17 Spectrum Melrose @ Robertson	18
19	20 City Holiday - No Work	21 Spectrum Melrose @ Robertson SoCal Gas @ W Knoll Spectrum on Westbourne Stage 5 - Sidewalk bands La Peer Storm Drain (begin)	22 SoCal Gas @ W Knoll Spectrum on Westbourne Stage 5 - Sidewalks	23 SoCal Gas @ W Knoll Spectrum on Westbourne	24 SoCal Gas @ W Knoll	25
26	27 SoCal Gas @ W Knoll Stage 5 - Sidewalks Stage 5 - Irrigation	28 Stage 5 - Sidewalks Stage 5 - Irrigation	1 Stage 5 - Sidewalks Stage 5 - Irrigation	2 Stage 5 - Sidewalks Stage 5 - Irrigation	3 Stage 5 - Irrigation	4

Stage Sequencing

Tentative Start Dates

Stage 4: March/April 2023

Stage 2: June/July 2023

Working Hours: 8AM – 5PM
Monday – Friday





Construction Activities Per Stage:

1. Tree Removal
2. Set up traffic control
3. Removals
 - Concrete sidewalks
 - Curb & gutter
 - Driveways
 - Asphalt roadway pavement
4. Utility work
5. Replace concrete & asphalt
6. Striping (painting) of new traffic lanes, parking spaces, and road markings

Norwich Gathering Space



Example of a shaded “stroll” design

Norwich Gathering Space --- Public Meetings

Plummer Park
Community Center
7377 Santa Monica
Boulevard
Rooms 5 and 6

Urban Arts Subcommittee (Concept Art Plan)

Thurs. Nov. 10, 2022 | 5pm

Arts and Cultural Affairs Commission

Thurs. Nov. 17, 2022 | 5pm

Urban Arts Subcommittee (Final Art Plan)

Thurs. Jan. 19, 2023 | 5pm

Arts and Cultural Affairs Commission

Thurs. Jan. 26, 2023 | 5pm

City Council Consideration

Feb. 23, 2023

www.weho.org/calendar.




Bus Shelters



- 2
- New Deco roof light
 - New Roof edge light
 - New Real time bus info screen
 - New USB Port
 - New Communication Cabinet
 - Replace existing screen and housing with new Digital screens (2)/housing



Bus Shelters

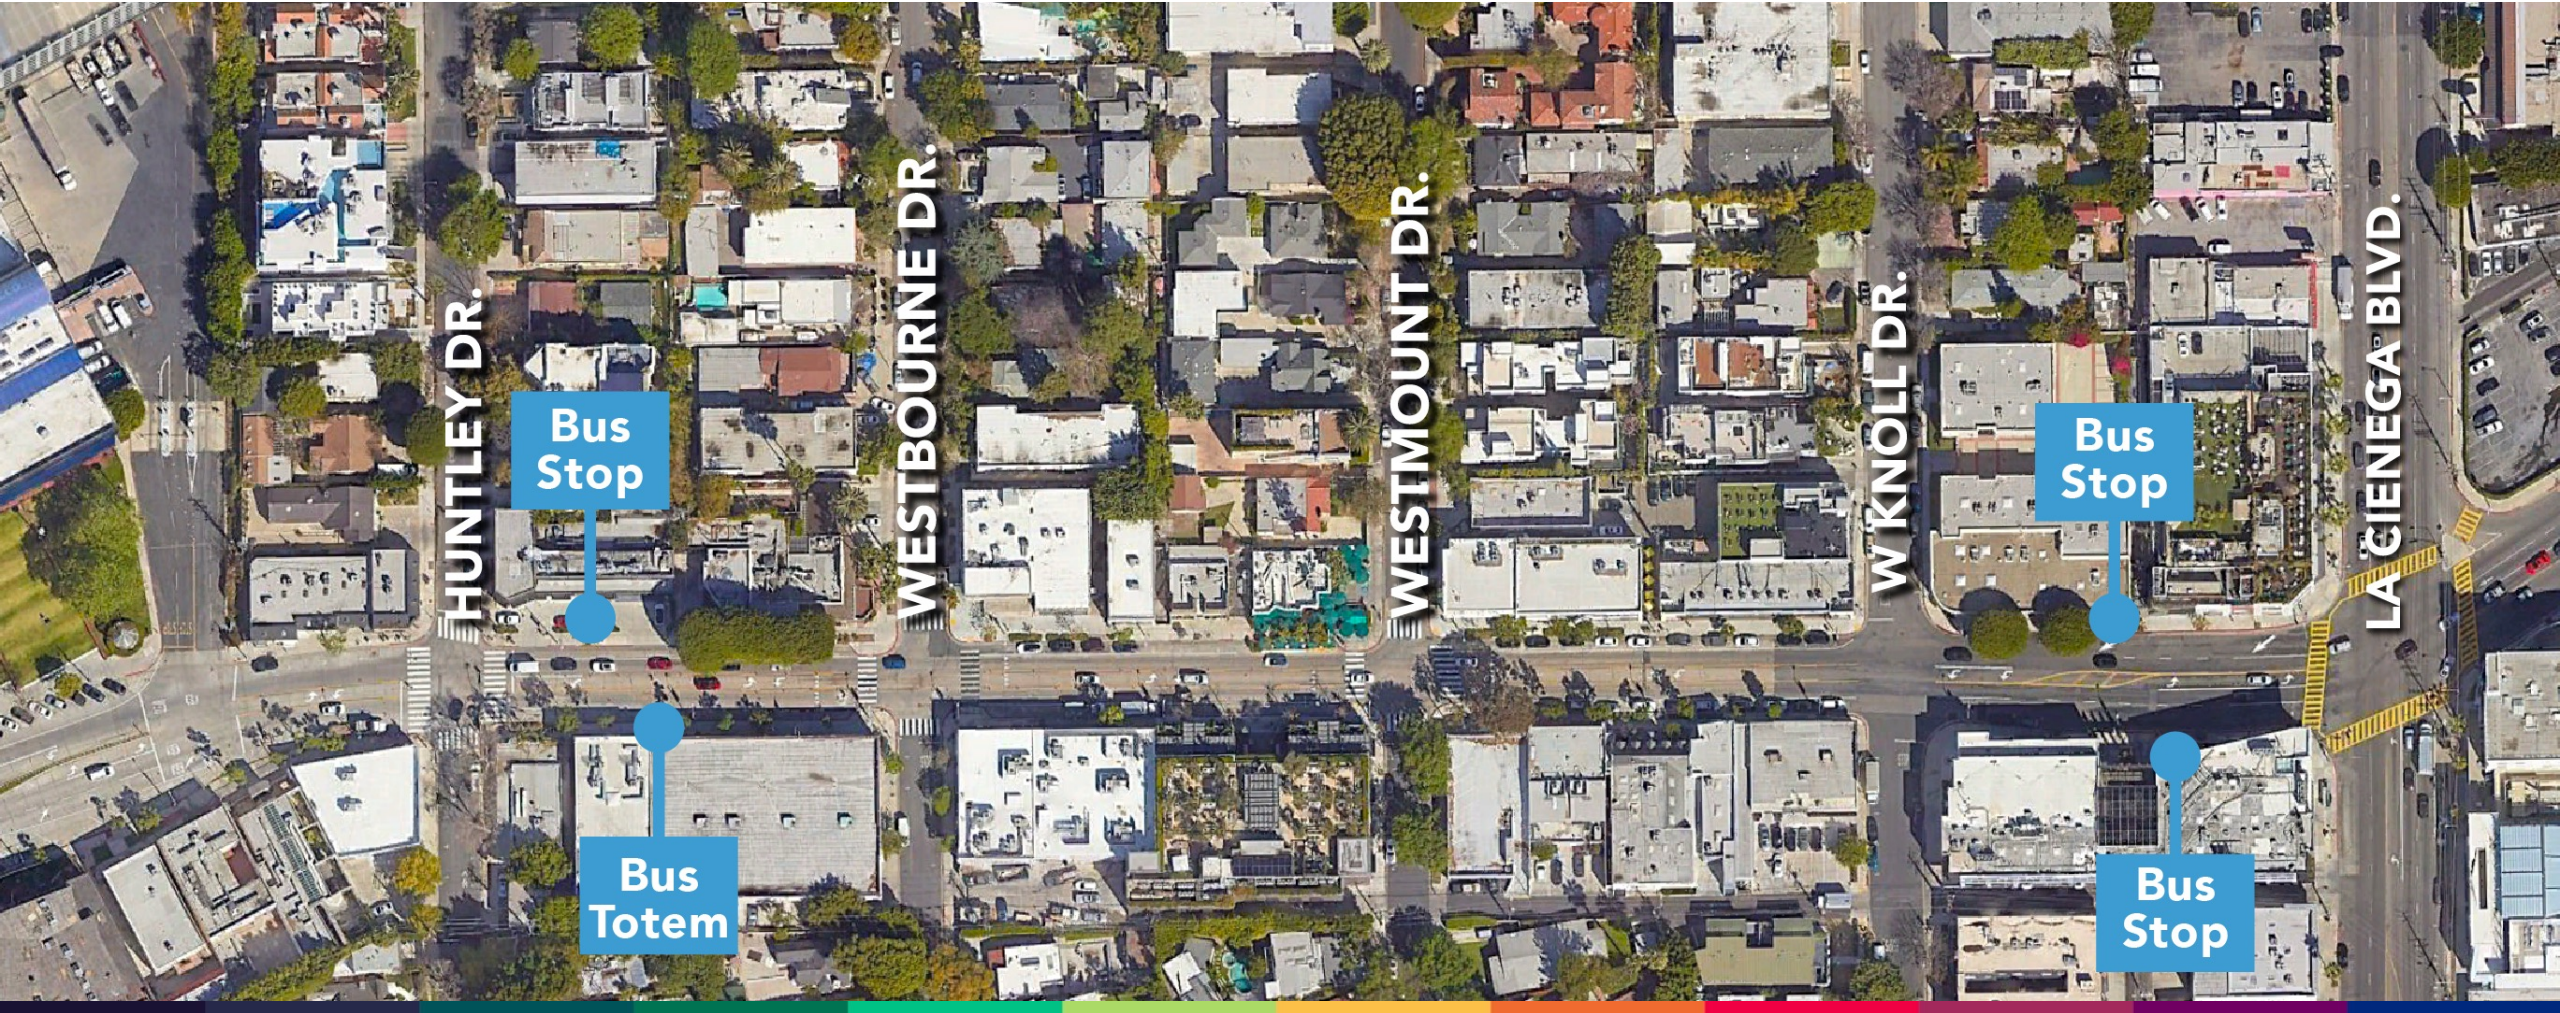

Final Construction Activities

- Irrigation system & testing
- Fiber optic cabling & splicing
- Landscape & lighting power
- Benches & bike racks
- Final asphalt grinding, paving & striping





JOIN OUR MAILING LIST

Email Us

WeHoDesignDistrictStreetscape
@bergcm.com



GIVE US FEEDBACK

Project Feedback Line

1 (800) 362-3996



VISIT OUR WEBSITE

Project Website

[WeHoDesignDistrictStreetscape.com](https://www.WeHoDesignDistrictStreetscape.com)



QUESTIONS
