



City of West Hollywood
California 1984

WEHO | DESIGN DISTRICT STREETSCAPE


Construction Updates
March 16, 2023





IMPROVEMENT PHASES


- Streetscape Phases
 - Phase 2 (5/22 – 12/23)
 - Phase 3 (2025)
 - Phase 5 (2026)
- Underground Phases
 - Phase 1A
Undergrounding (Melrose) (4/22 – 5/23)
 - Phase 1B
Undergrounding (Almont + La Peer) (23 – 24)
 - Phase 4
Undergrounding (2025)

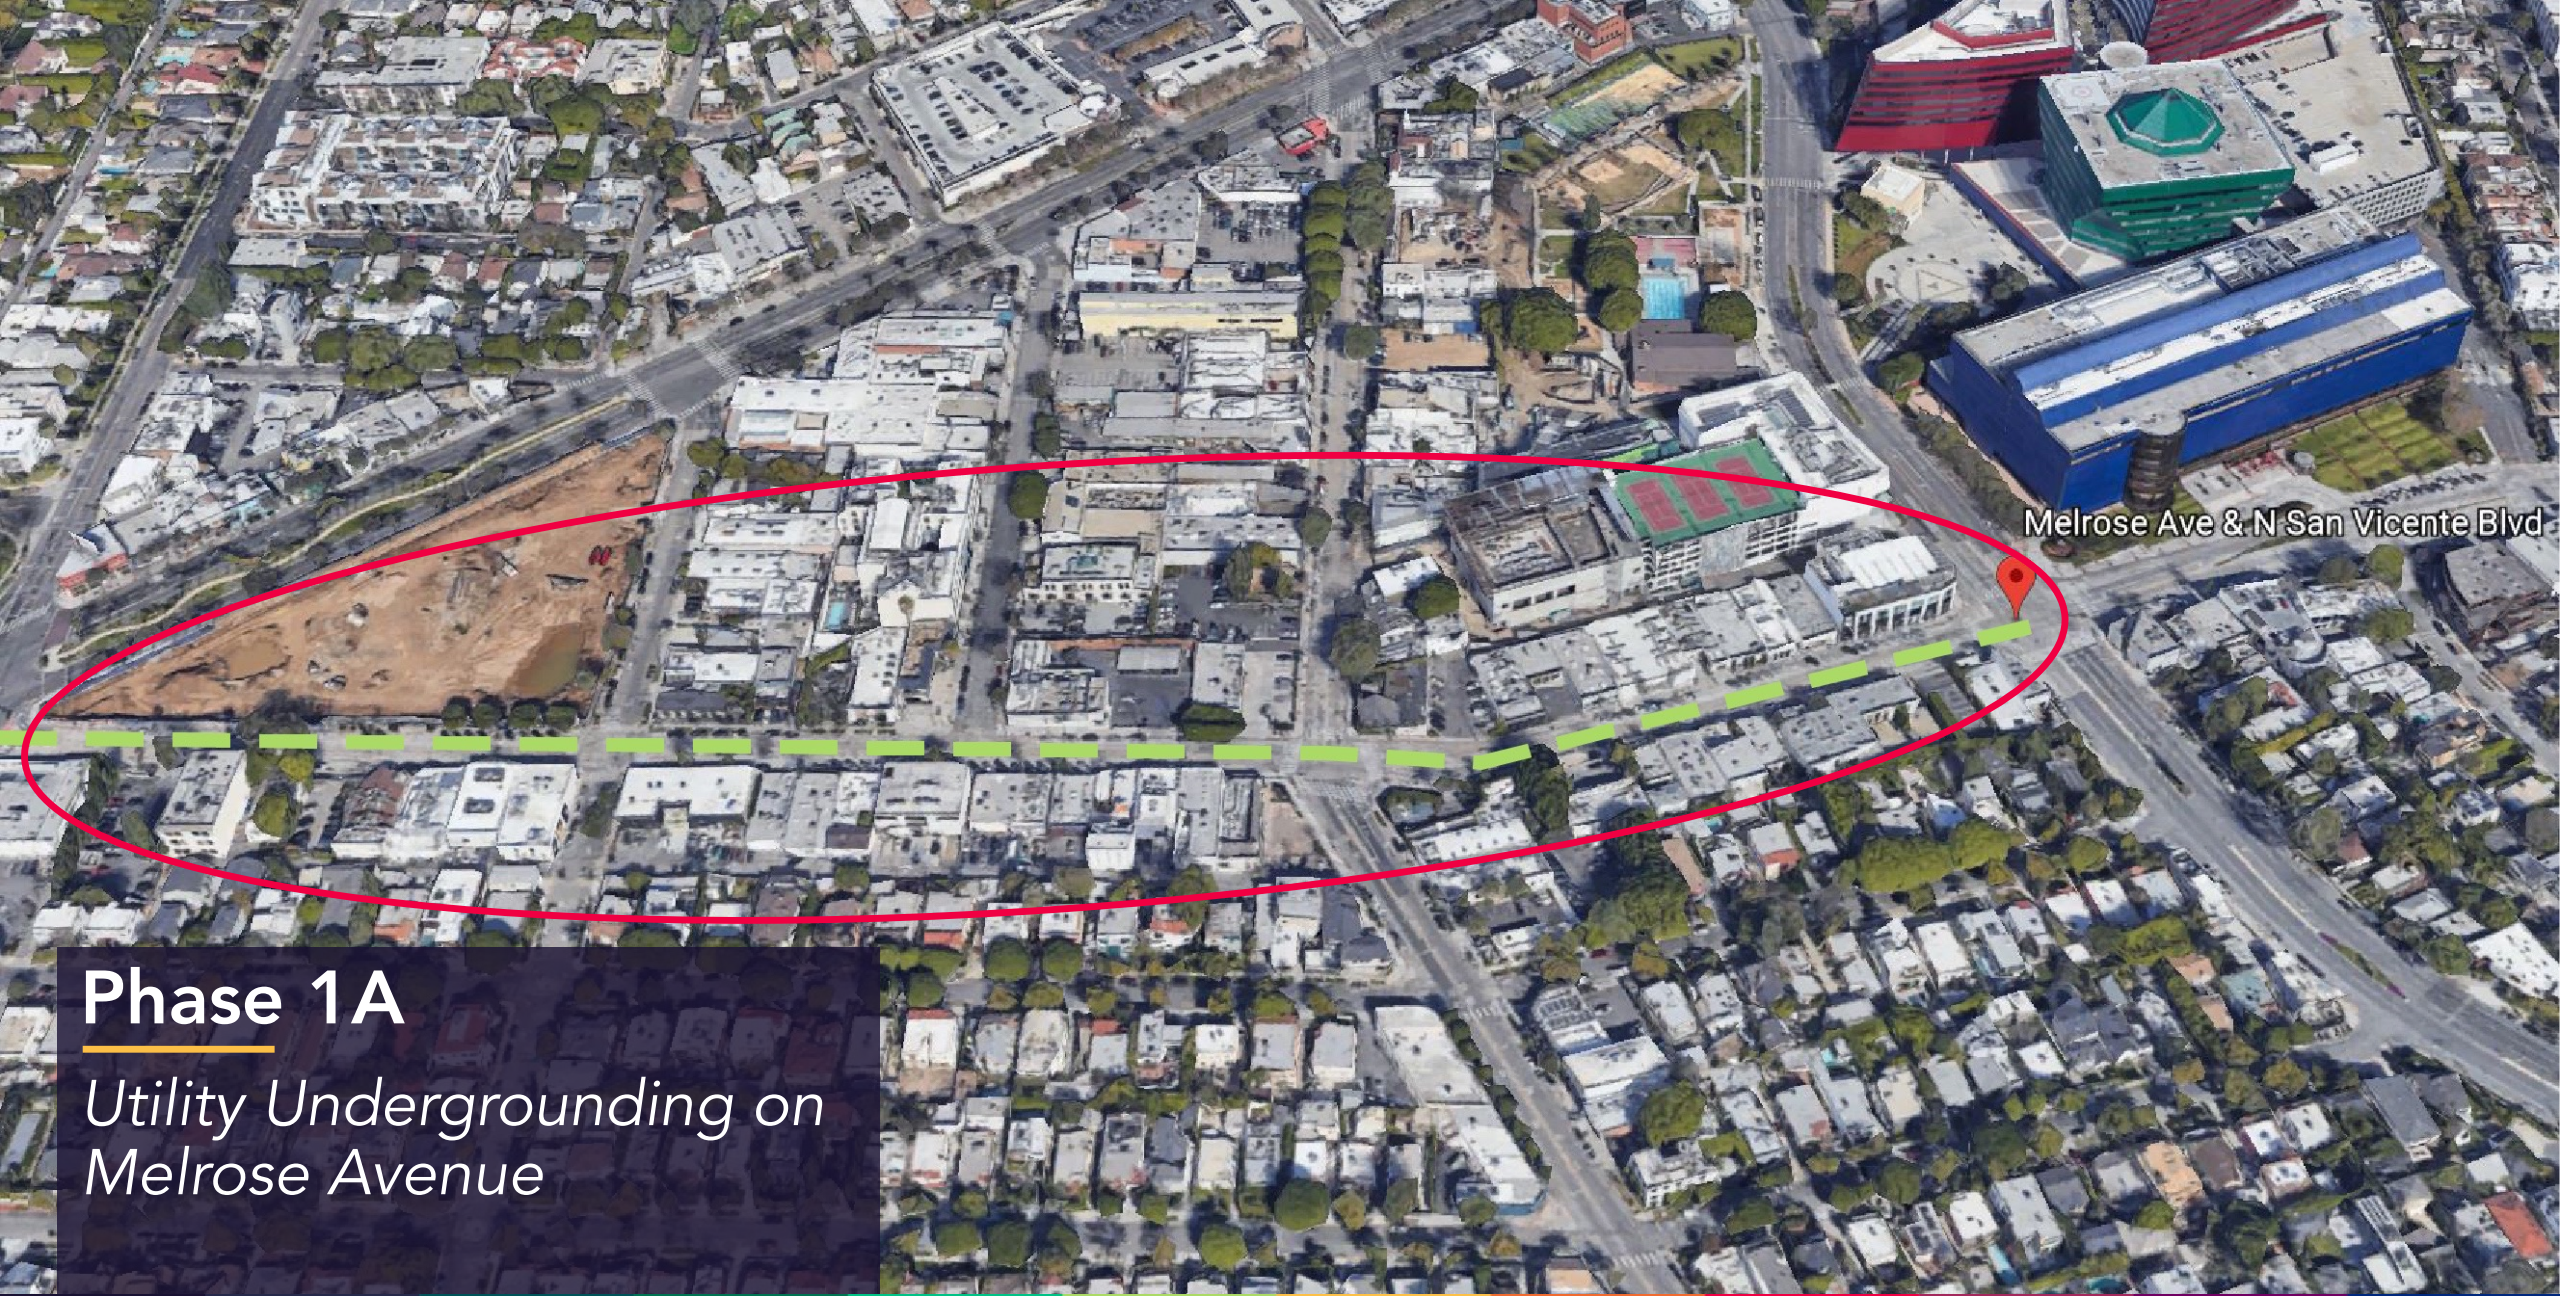

Melrose Ave & N San Vicente Blvd

Phase 1A

*Utility Undergrounding on
Melrose Avenue*

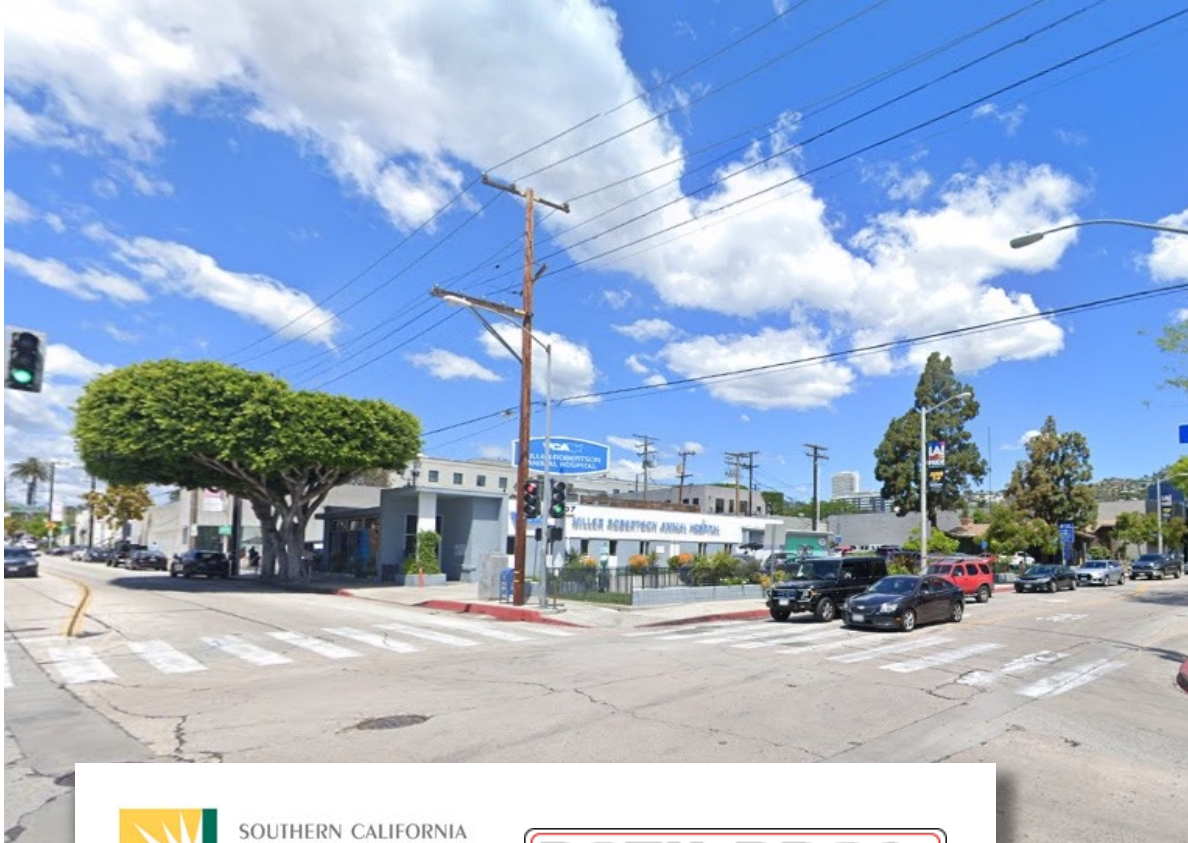

Utility Undergrounding

Southern California Edison (SCE) is leading the utility undergrounding phase in cooperation with the City of West Hollywood and Berg.



West Hollywood Park

Grassy grounds with a playground & pool

West Hollywood Library

The Center for Early Education

Rosewood STEM Magnet

Phase 2

Streetscape on Melrose Avenue

An aerial photograph of a city street, La Cienega Blvd, running vertically. A large orange diagonal banner is overlaid across the street, with a green oval at its top end. The banner is divided into two sections: the upper section is labeled 'NORTH SIDE' and the lower section is labeled 'SOUTH SIDE'. The street is lined with buildings, parking lots, and trees. A white text box in the bottom right corner contains project details. A colorful horizontal bar is at the very bottom of the image.

LA CIENEGA BLVD

NORTH SIDE
SOUTH SIDE

CROFT AVE

Start: October 6, 2022

South Side: Approx. 3.5 months

North Side: Approx. 3 months

Working Hours: 8AM – 5PM

Monday – Friday

Stage 5 Partial Completion

(What will Stage 5 look like when contractor mobilizes to next stage?)

- No barriers
- 2 lanes of traffic in each direction (with exception of median lane closures)
- Metered parking on both sides of street
- Cones will remain in landscape planters (trip hazard)



Stage Sequencing

Tentative Start Dates

Stage 4: End of March 2023

Stage 2: June/July 2023

Working Hours: 8AM – 5PM

Monday – Friday






Construction Activities Per Stage:

1. Set up traffic control (March 27 & 28)
2. Saw-cutting (noise)
3. Tree removal
4. Removals
 - Concrete sidewalks
 - Curb & gutter
 - Driveways
 - Asphalt roadway pavement
4. Utility work
5. Replace concrete & asphalt
6. Striping (painting) of new traffic lanes, parking spaces, and road markings

Stage 4 Traffic:

- One lane in each direction from Huntley Dr to La Cienega
- No parking on south side of street between Westbourne and La Cienega
- Parking will remain on north side of street
- Pedestrian walkway (shown in blue)

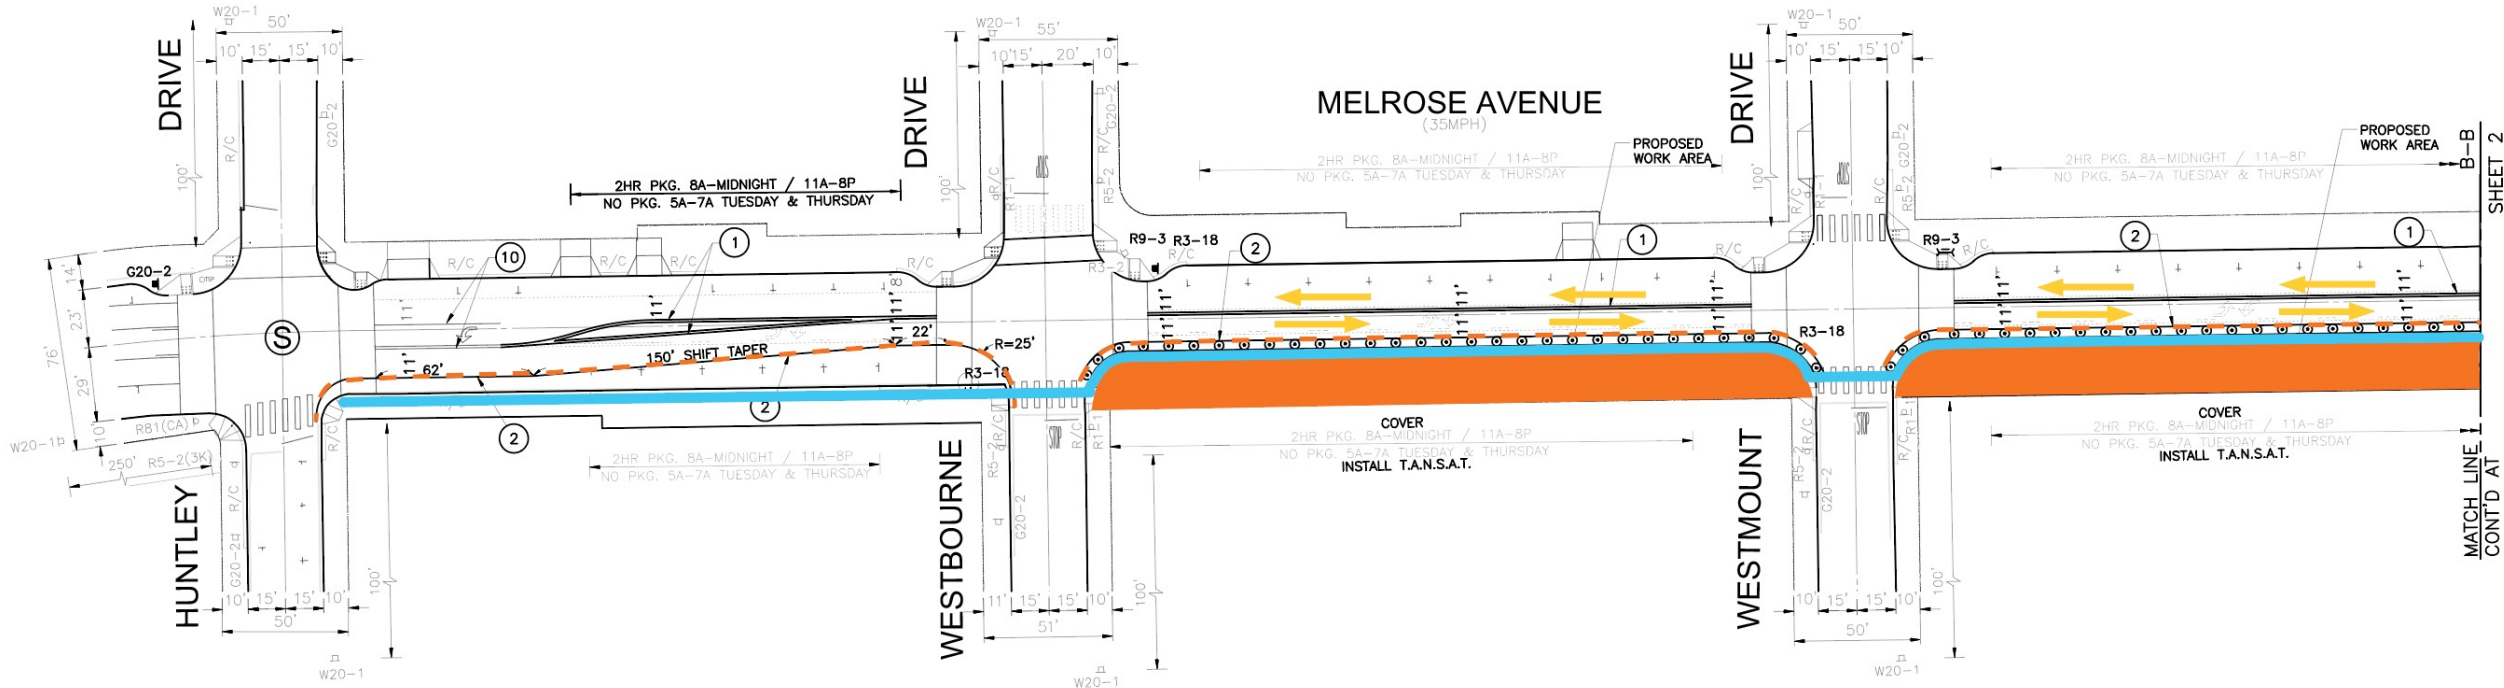

Tentative Schedule – Weather Pending

March 2023

February '23							April '23						
S	M	T	W	T	F	S	S	M	T	W	T	F	S
			1	2	3	4							1
5	6	7	8	9	10	11	2	3	4	5	6	7	8
12	13	14	15	16	17	18	9	10	11	12	13	14	15
19	20	21	22	23	24	25	16	17	18	19	20	21	22
26	27	28					23	24	25	26	27	28	29
							30						

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
12	13	14 Rain	15 Rain	16 Gathering Space Final Plan: Urban Arts Subcommittee	17 Stage 5 - Paver Installation	18
19	20 Stage 5 - Paver Installation	21 Stage 5 - Paver Installation	22 Stage 5 - Paver Installation	23 Utilities Gathering space review by Cultural Affairs	24 Utilities	25
26	27 Stage 5 Barricades Removal Stage 4 Barricade Set-up	28 Stage 5 Barricades Removal & Parking Restored Stage 4 Barricade Set-up & Saw-cutting	29 Stage 4 Saw-cutting	30 Stage 4 Tree Removals, saw-cutting, & sidewalk demo	31 Stage 4 Tree Removals, saw-cutting, & sidewalk demo	1

Private Developer Work La Peer Dr Storm Drain

March 6, 2023 – June 9, 2023



Norwich Gathering Space



Norwich Gathering Space

Public Meetings

Plummer Park
Community Center
7377 Santa Monica
Boulevard
Rooms 5 and 6

Urban Arts Subcommittee (Concept Art Plan)

Thurs. Nov. 10, 2022 | 5pm

Arts and Cultural Affairs Commission

Thurs. Nov. 17, 2022 | 5pm

Urban Arts Subcommittee (Final Art Plan)

Thurs. Jan. 19, 2023 | 5pm

Arts and Cultural Affairs Commission

Thurs. Jan. 26, 2023 | 5pm

City Council Consideration


Feb. 23, 2023

Urban Arts Subcommittee (Final Art Plan)

Thurs. March 16, 2023 | 5pm

www.weho.org/calendar


Bus Shelters

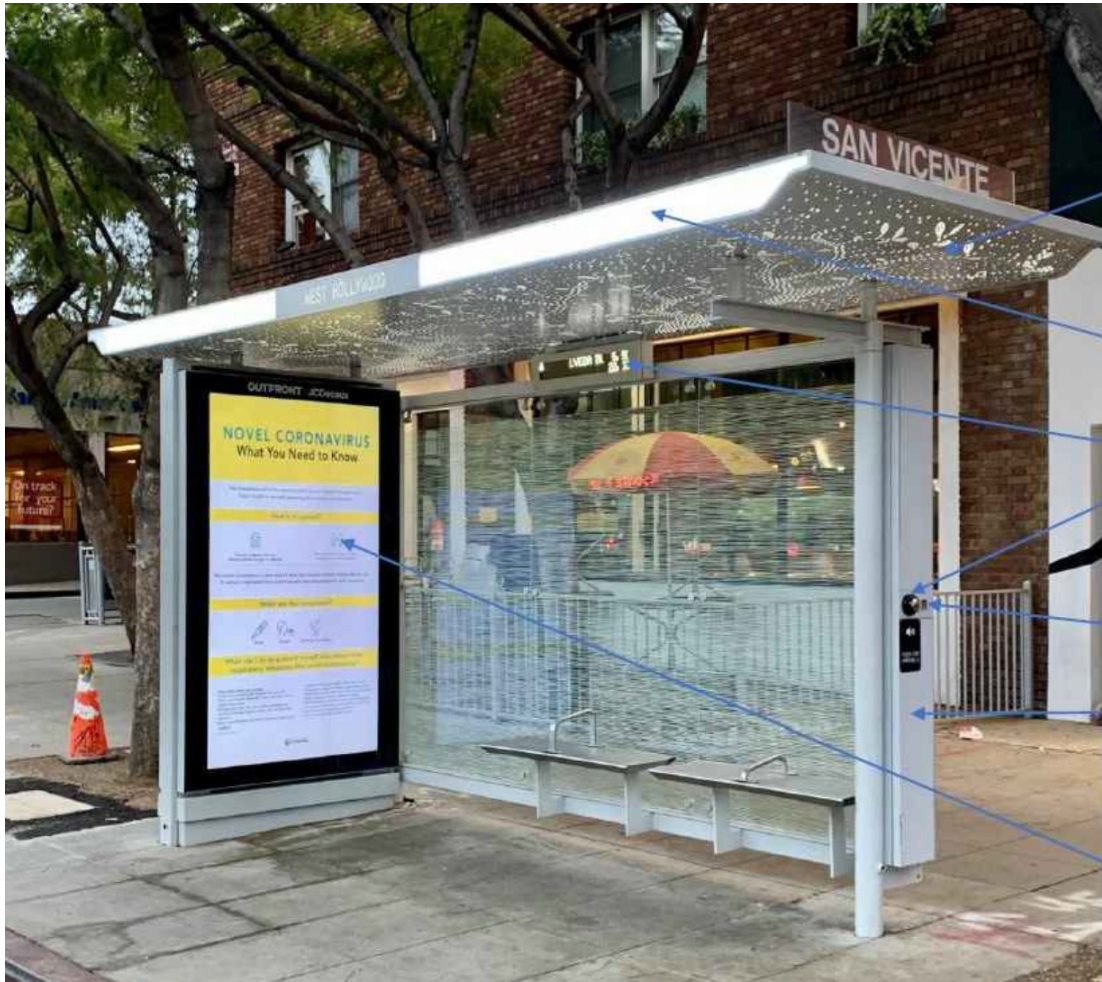

- 2
- New Deco roof light
 - New Roof edge light
 - New Real time bus info screen
 - New USB Port
 - New Communication Cabinet
 - Replace existing screen and housing with new Digital screens (2)/housing



Bus Shelters

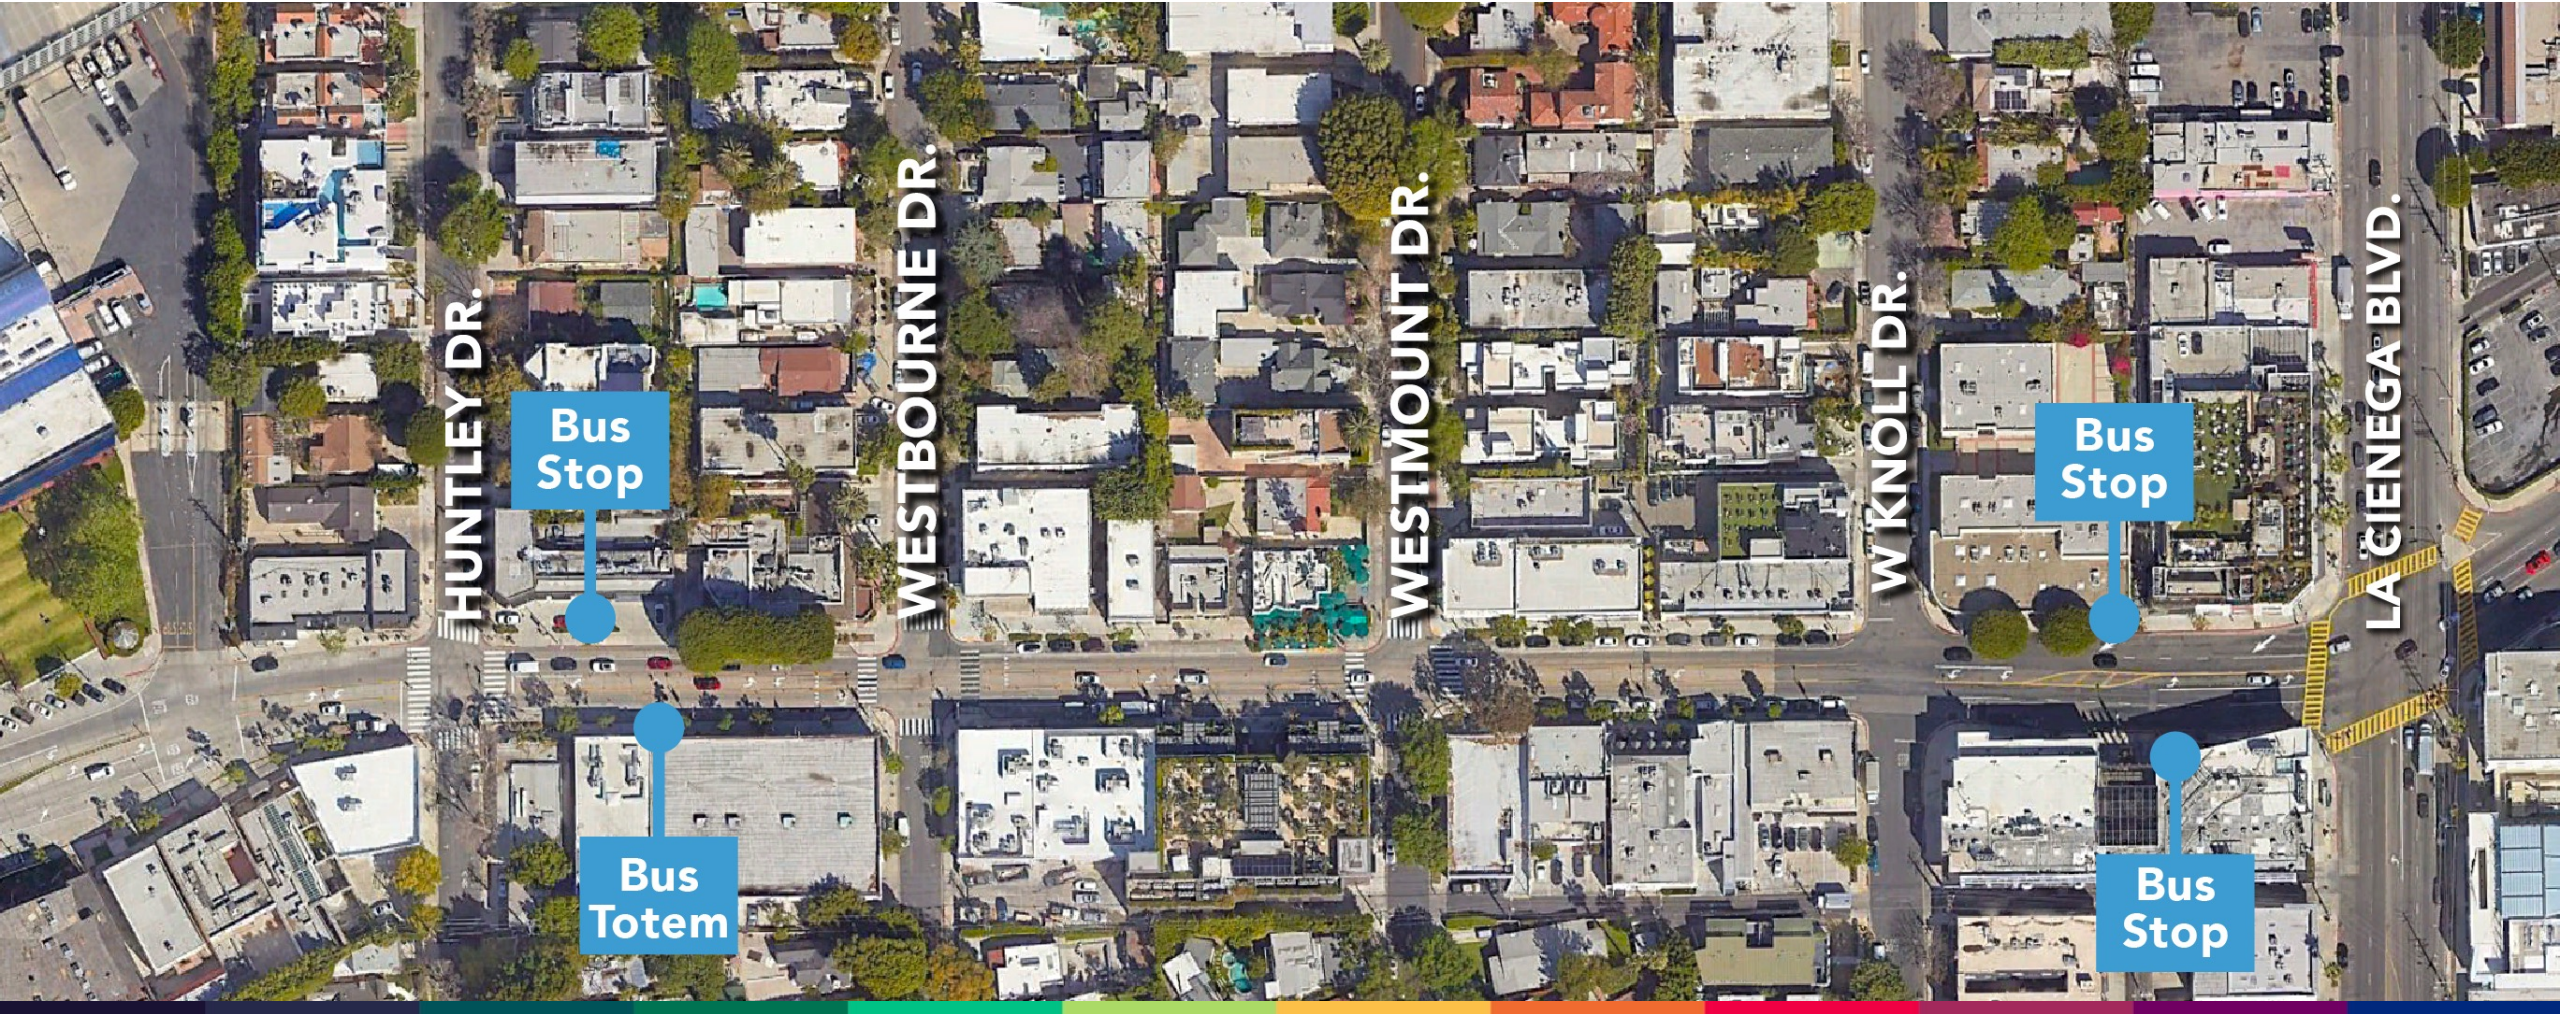

Final Construction Activities

- Irrigation system & testing
- Fiber optic cabling & splicing
- Landscape & lighting power
- Benches & bike racks
- Final asphalt grinding, paving & striping





JOIN OUR MAILING LIST

Email Us

WeHoDesignDistrictStreetscape
@bergcm.com



GIVE US FEEDBACK

Project Feedback Line

1 (800) 362-3996



VISIT OUR WEBSITE

Project Website

WeHoDesignDistrictStreetscape.com

