



City of West Hollywood  
California 1984

# WEHO | DESIGN DISTRICT STREETSCAPE

Construction Updates  
March 16, 2023



An aerial photograph of a city street intersection. A large orange diagonal band runs from the bottom-left towards the top-right. The band is divided into two sections: the upper section is labeled 'NORTH SIDE' and the lower section is labeled 'SOUTH SIDE'. A green oval is located in the upper right portion of the orange band. The street is labeled 'LA CIENEGA BLVD' on the left and 'CROFT AVE' on the right. The surrounding area includes various buildings, parking lots, and trees.

LA CIENEGA BLVD

NORTH SIDE  
SOUTH SIDE

CROFT AVE

**Start:** October 6, 2022

**South Side:** Approx. 3.5 months


**North Side:** Approx. 3 months

**Working Hours:** 8AM – 5PM

Monday – Friday

## Stage 5 Median:

- One week duration
- Start date TBD
- Daily lane closures between 9am – 4pm
- One lane in each direction in construction area

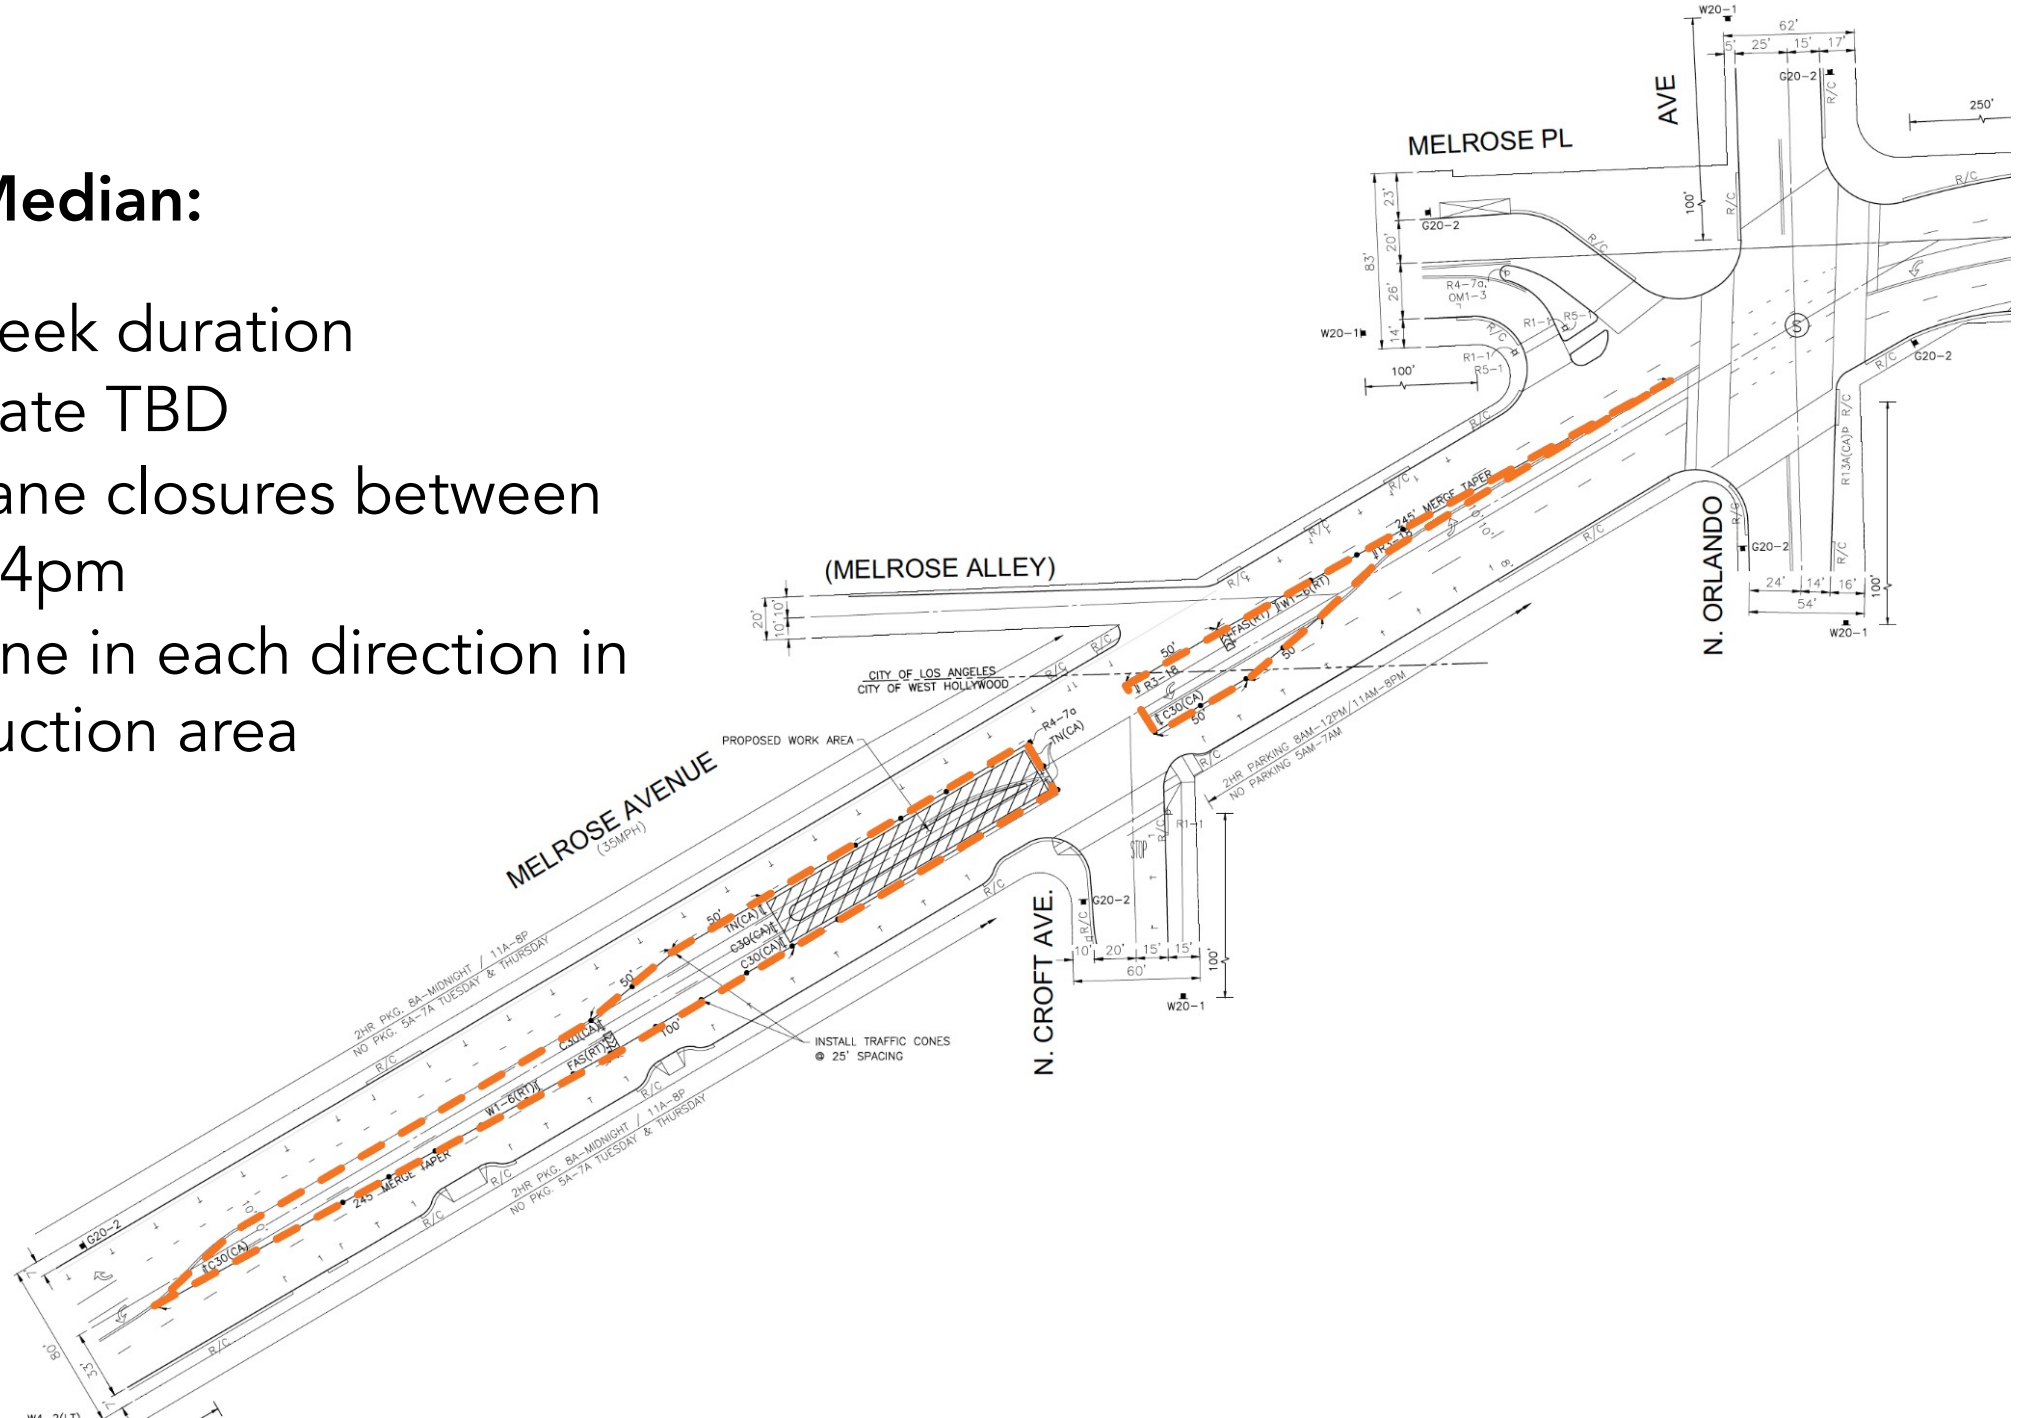

## Stage 5 Partial Completion

(What will Stage 5 look like when contractor mobilizes to next stage?)

- No barriers
- 2 lanes of traffic in each direction (with exception of median lane closures)
- Metered parking on both sides of street
- Cones will remain in landscape planters (trip hazard)



# Stage Sequencing

## Tentative Start Dates

**Stage 4:** End of March 2023

**Stage 2:** June/July 2023

**Working Hours:** 8AM – 5PM  
Monday – Friday






## Construction Activities Per Stage:

1. Set up traffic control (March 27 & 28)
2. Saw-cutting (noise)
3. Tree removal
4. Removals
  - Concrete sidewalks
  - Curb & gutter
  - Driveways
  - Asphalt roadway pavement
4. Utility work
5. Replace concrete & asphalt
6. Striping (painting) of new traffic lanes, parking spaces, and road markings

## Stage 4 Traffic:

- One lane in each direction from Huntley Dr to La Cienega
- No parking on south side of street between Westbourne and La Cienega
- Parking will remain on north side of street
- Pedestrian walkway (shown in blue)

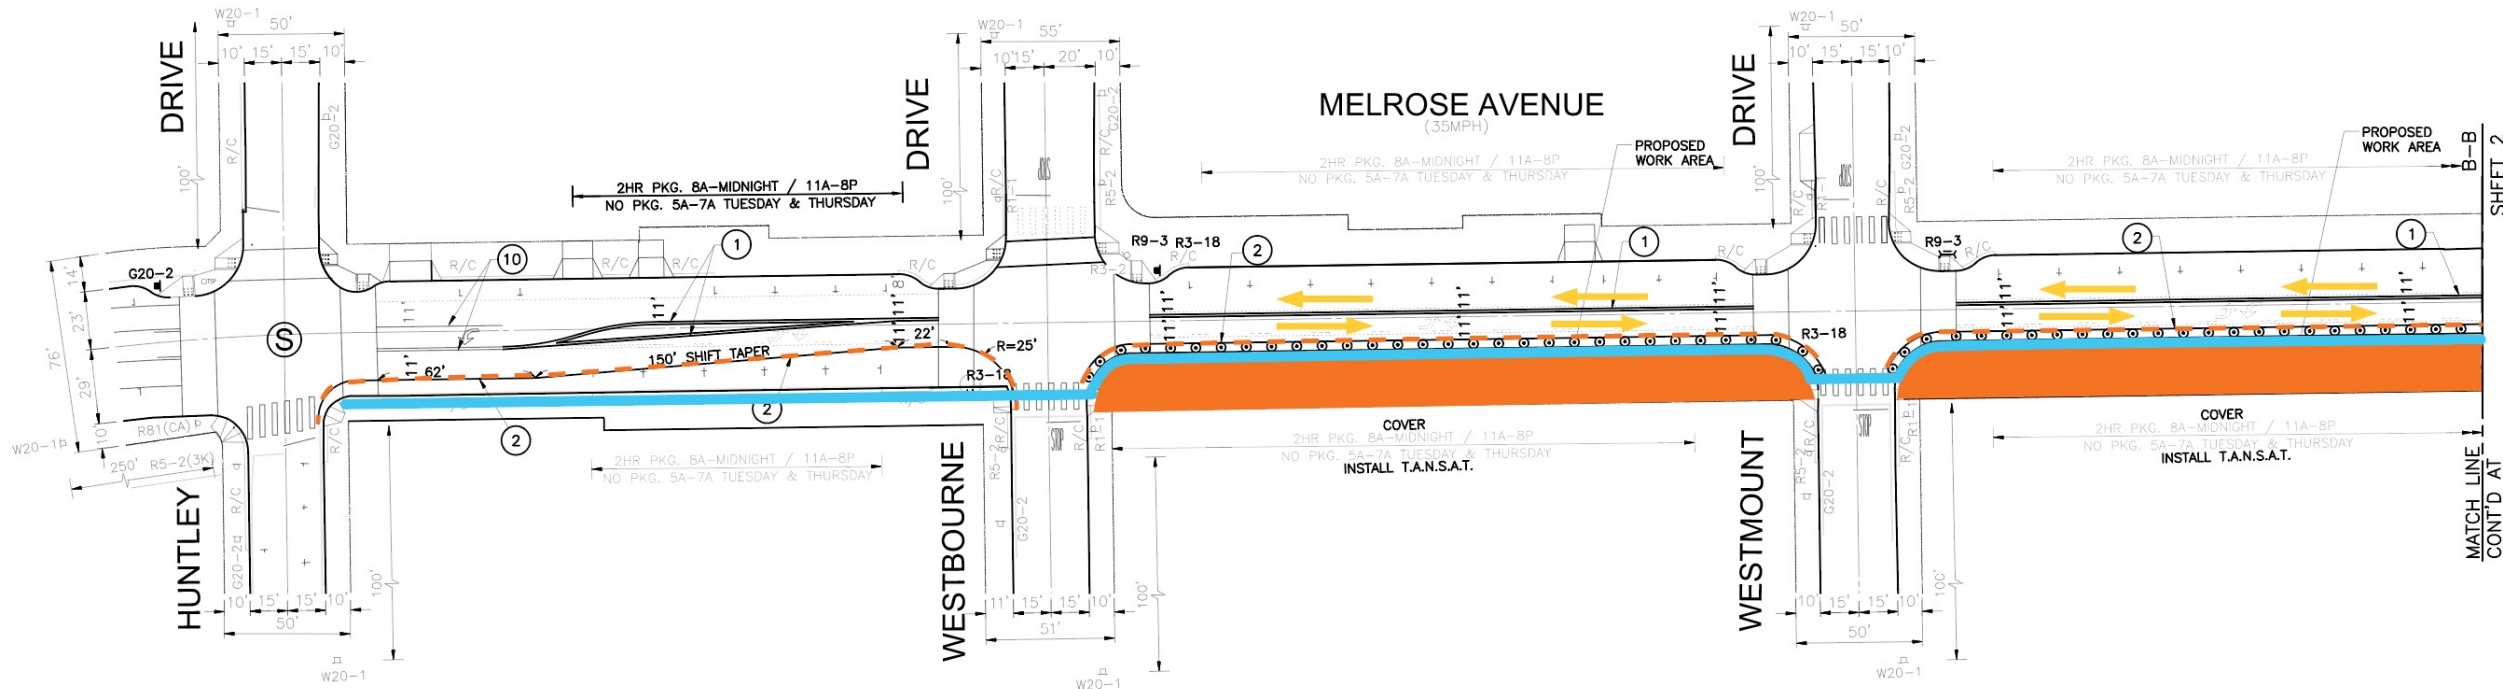

*Tentative Schedule – Weather Pending*

# March 2023

February '23							April '23						
S	M	T	W	T	F	S	S	M	T	W	T	F	S
			1	2	3	4							1
5	6	7	8	9	10	11	2	3	4	5	6	7	8
12	13	14	15	16	17	18	9	10	11	12	13	14	15
19	20	21	22	23	24	25	16	17	18	19	20	21	22
26	27	28					23	24	25	26	27	28	29
							30						

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
<b>12</b>	<b>13</b>	<b>14</b>  Rain	<b>15</b>  Rain	<b>16</b>  Gathering Space Final Plan: Urban Arts Subcommittee	<b>17</b>  Stage 5 - Paver Installation	<b>18</b>
<b>19</b>	<b>20</b>  Stage 5 - Paver Installation	<b>21</b>  Stage 5 - Paver Installation	<b>22</b>  Stage 5 - Paver Installation	<b>23</b>  Utilities  Gathering space review by Cultural Affairs	<b>24</b>  Utilities	<b>25</b>
<b>26</b>	<b>27</b>  Stage 5 Barricades Removal  Stage 4 Barricade Set-up	<b>28</b>  Stage 5 Barricades Removal & Parking Restored Stage 4 Barricade Set-up & Saw-cutting	<b>29</b>  Stage 4 Saw-cutting	<b>30</b>  Stage 4 Tree Removals, saw-cutting, & sidewalk demo	<b>31</b>  Stage 4 Tree Removals, saw-cutting, & sidewalk demo	<b>1</b>
