




City of West Hollywood
California 1984

WEHO | DESIGN DISTRICT STREETSCAPE


Construction Updates
July 20, 2023



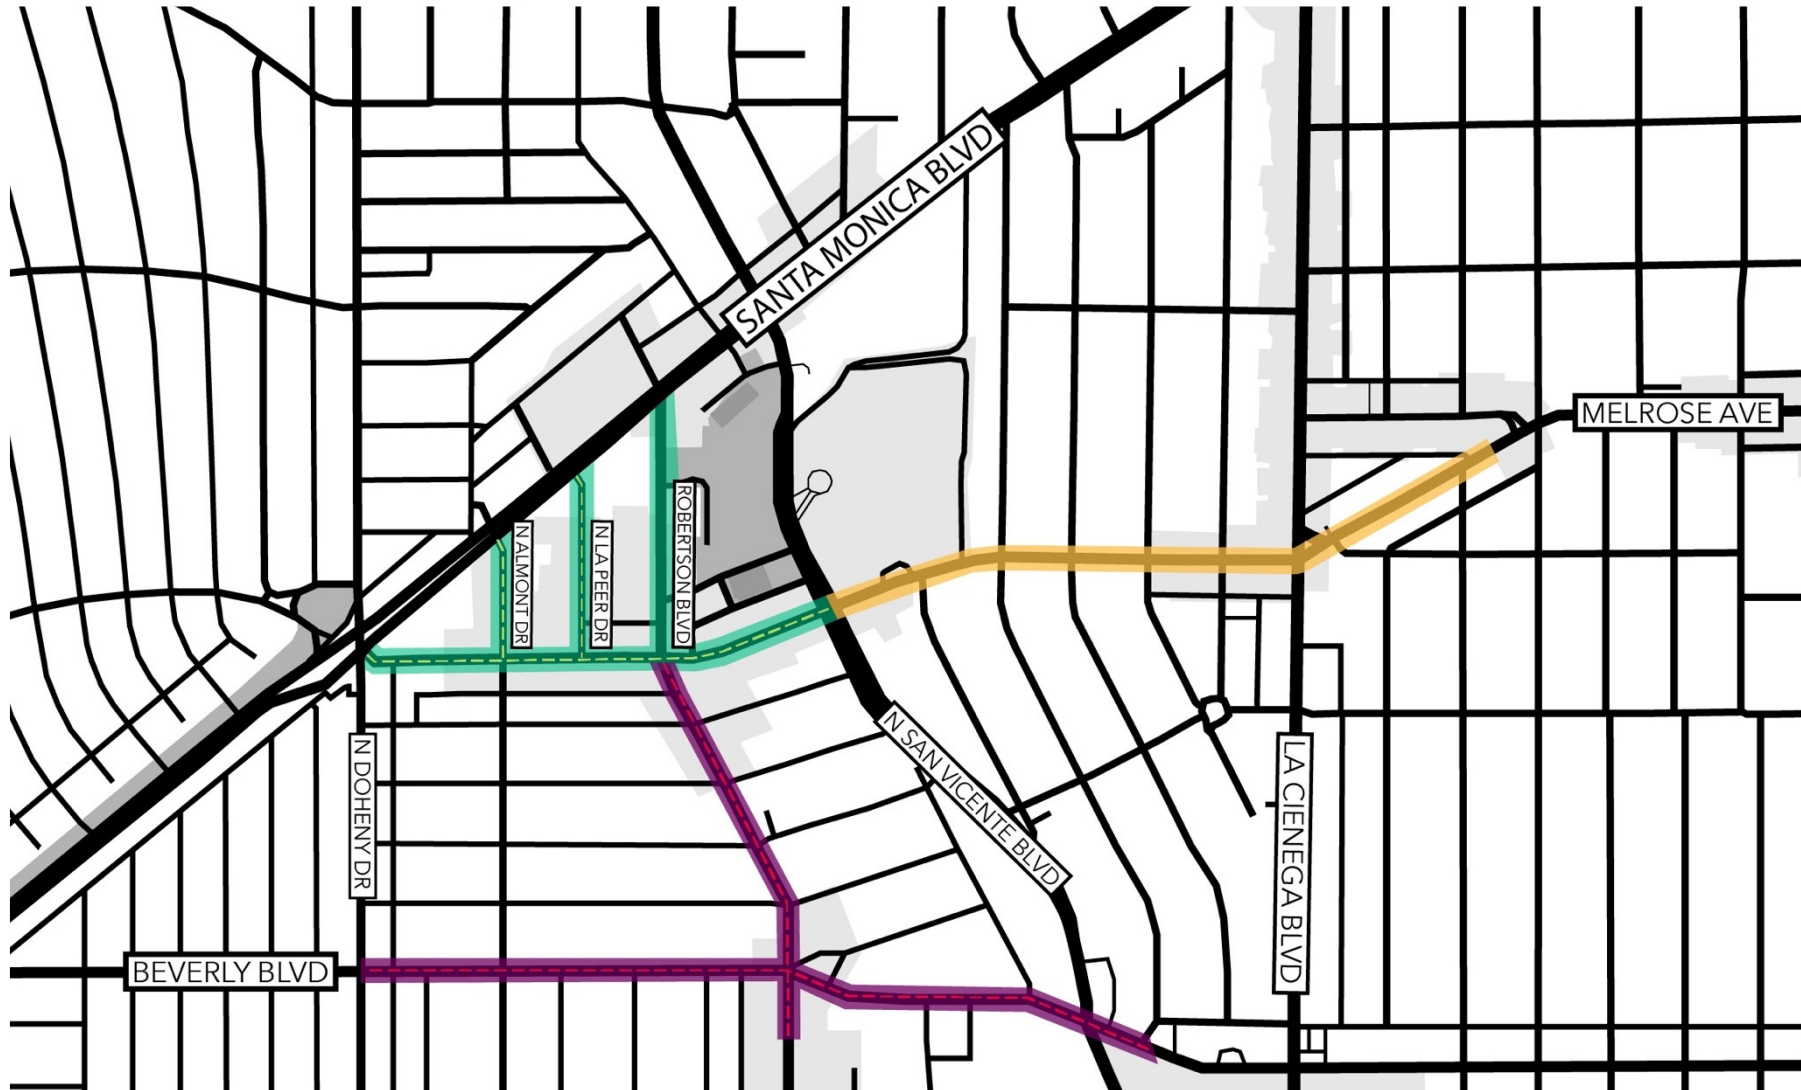

IMPROVEMENT PHASES

- Streetscape Phases
- Phase 2 (5/22 – 12/23)
 - Phase 3 (2025)
 - Phase 5 (2026)
- Underground Phases
- Phase 1A
Undergrounding
(Melrose) (4/22 – 5/23)
 - Phase 1B
Undergrounding
(Almont + La Peer) (23 – 24)
 - Phase 4
Undergrounding (2025)

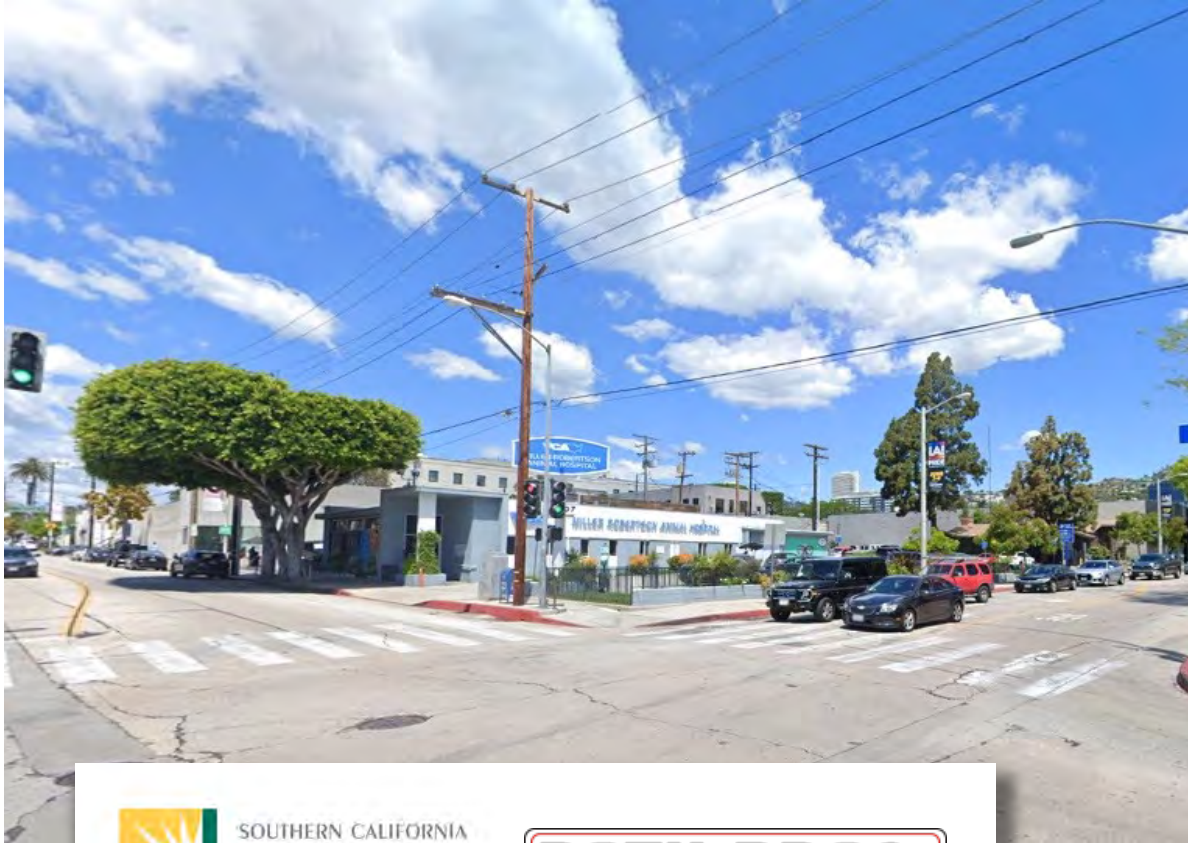

 SOUTHERN CALIFORNIA
EDISON
Energy for What's Ahead®

DOTY BROS.
Construction Company



Utility Undergrounding

Southern California Edison (SCE) is leading the utility undergrounding phase in cooperation with the City of West Hollywood and Berg.



West Hollywood Park

Grassy grounds with a playground & pool

West Hollywood Library

The Center for Early Education

Rosewood STEM Magnet

Phase 2

Streetscape on
Melrose Avenue

Staged Schedule

Stage 1: May 9, 2022 – Jul 2022

Stage 3: Jul 2022 – Oct 6, 2022

Stage 5 (South): Oct 6, 2023 – Dec 30, 2023

Stage 5 (North): Jan 3, 2023 – April 3, 2023

Stage 4: April 3, 2023 – June 28, 2023

Stage 2: June 28, 2023 – Oct 2022



Current Activities

Stage 2

Saw Cutting

- Complete

Concrete Sidewalk Removals

- 98% Complete (some curb & gutter remain)
- Concrete street removals approximately 6 weeks out



Current Activities

Expansive Soil Replacement

- Complete from San Vicente to east of Norwich
- Huntley to Westbourne began today. Continue tomorrow and into next week
- Norwich to Huntley is gathering space – excavation after Huntley to Westbourne



Next Week's Activities

Curb & Gutter

- Form and pour concrete curb and gutter beginning Monday, July 24, 2023
- Begin at San Vicente work east
- San Vicente to ~Norwich: Monday, July 24

Storm Drain

- Install 2 new catch basins east and west of Norwich week of July 24, 2023




Upcoming Activities

Utilities

- Beverly Hills Water to install and relocate meters
- AT&T relocate one cabinet in front of Hamilton Selway at San Vicente Blvd.



Stage 2

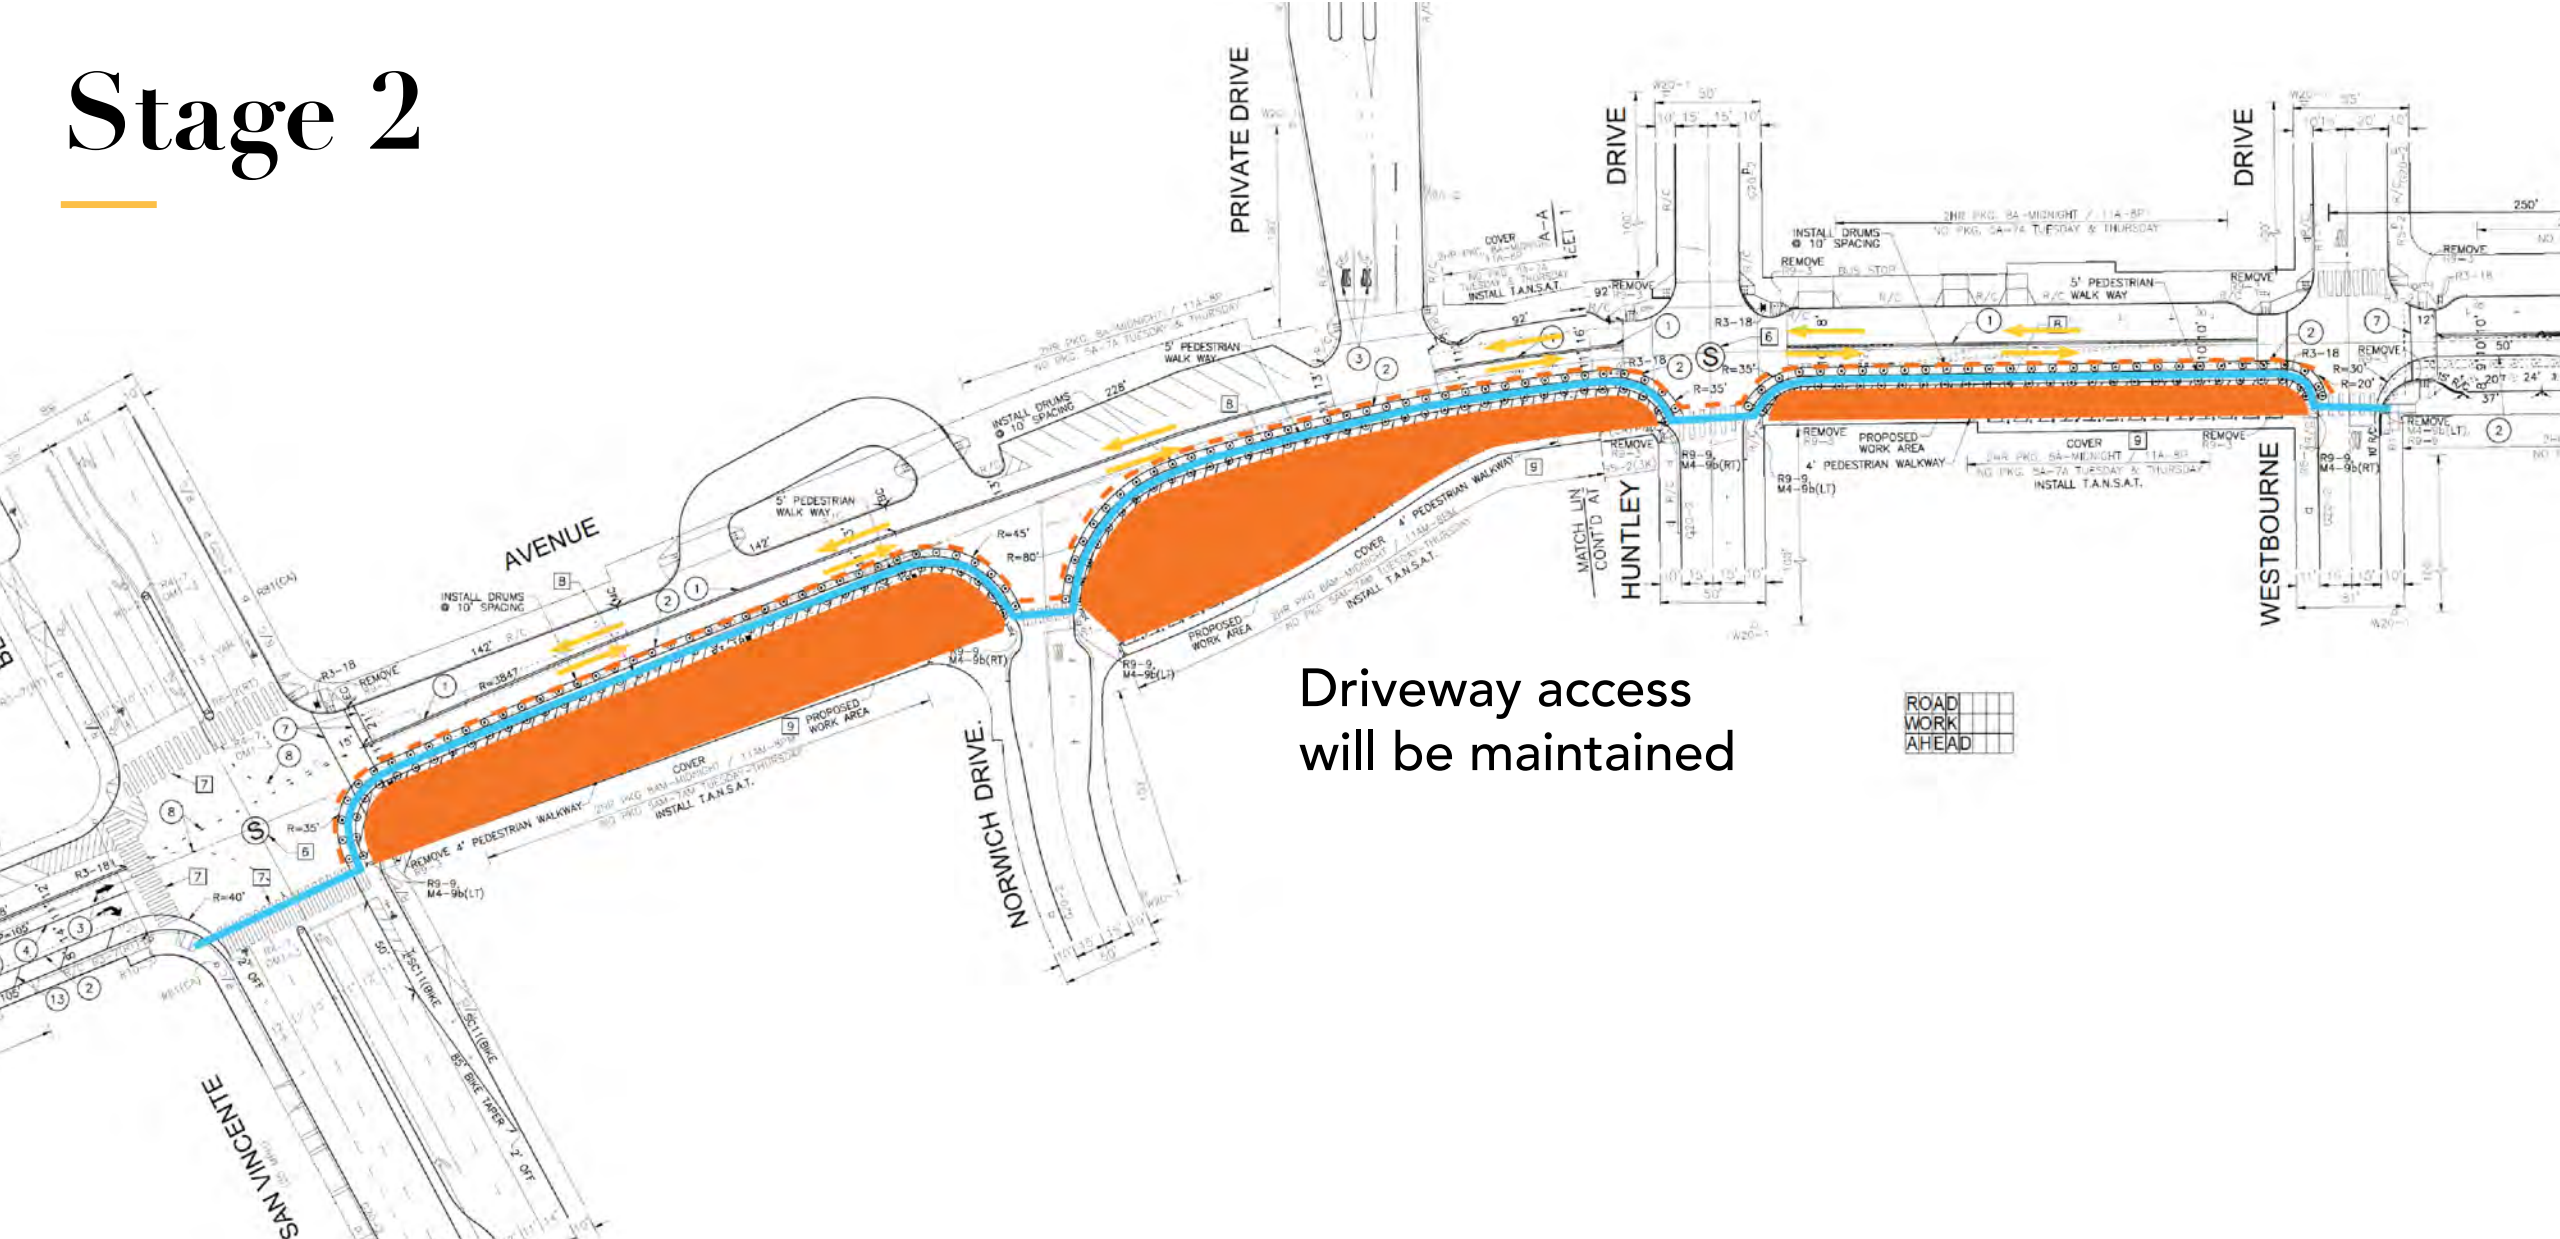

Driveway access
will be maintained

Parking Validation Program




Melrose
Streetscape
Parking Map

Validated Public Parking for **WEST HOLLYWOOD PARKING GARAGE** 625 N. SAN VICENTE BOULEVARD


Melrose Ave Validation Program

- 1-hour additional parking with validation (2-hours free total)
- Valid at City Structure 625 N San Vicente Blvd. only
- Scan QR code below to request validations tickets

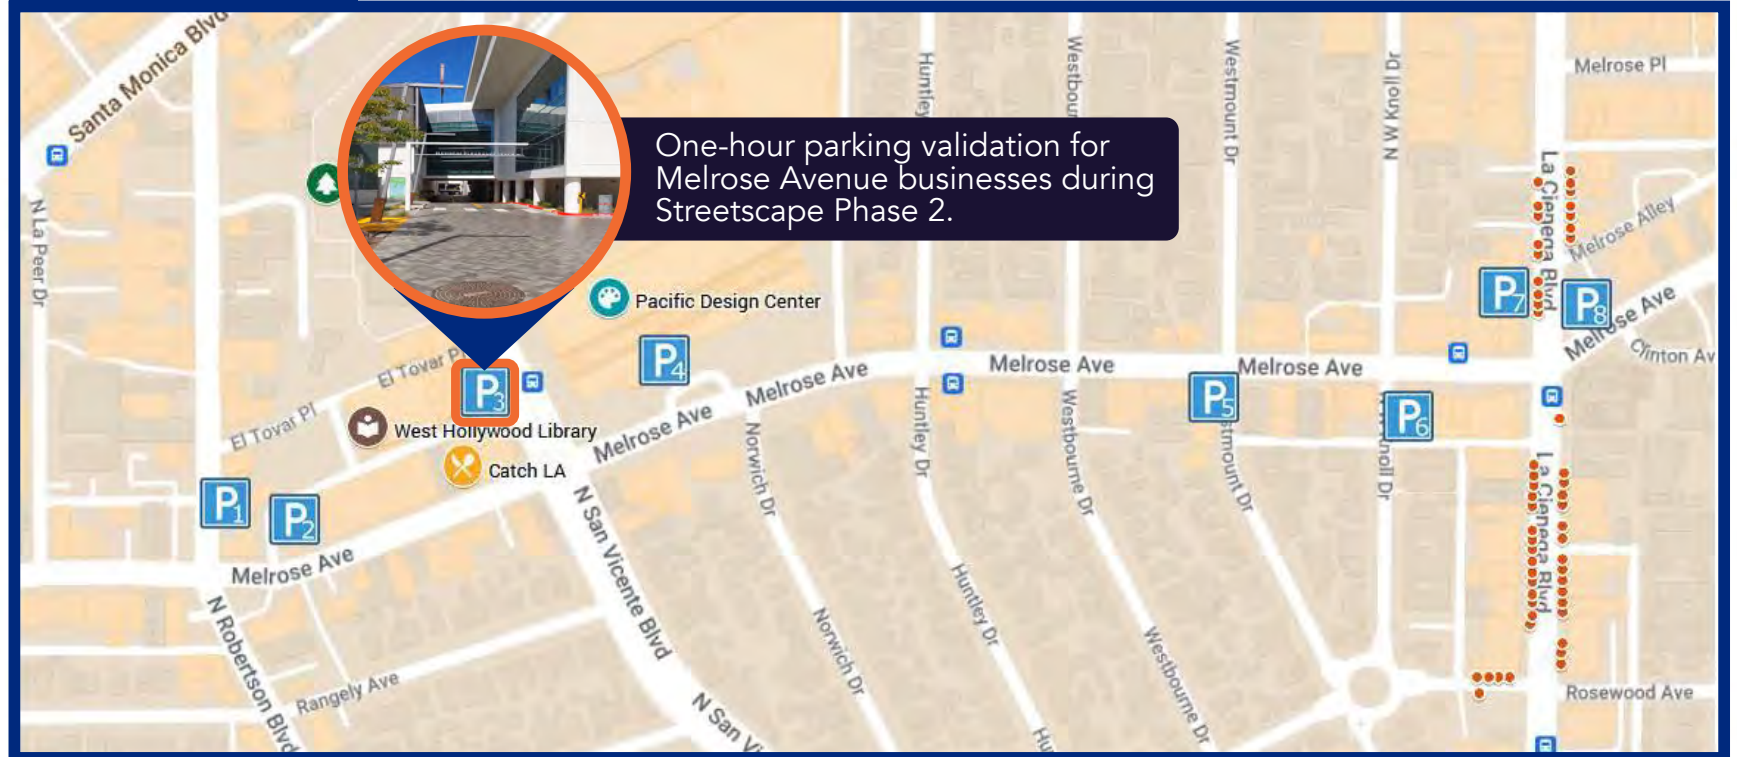

Residential Side Street Parking

- 2-hours of parking without a permit allowed on west side of residential streets south of Melrose Ave.
- Residential permit required on east side of street



Parking Options



PUBLIC VALET PARKING ONE

Location
567 Westmount Dr.
(Restoration Hardware)

Cost
\$5 for first 2 hours
\$15 after 2 hours

Duration
2-hours

Operating Hours
10:00am – 7:00pm

PUBLIC VALET PARKING TWO

Location
8565 Melrose Ave.
(Urth Caffe)

Cost
\$10

Duration
2-hours

Operating Hours
9:00am – 6:00pm

Norwich Gathering Space




Bus Shelters



- 2
- New Deco roof light
 - New Roof edge light
 - New Real time bus info screen
 - New USB Port
 - New Communication Cabinet
 - Replace existing screen and housing with new Digital screens (2)/housing



Bus Shelters

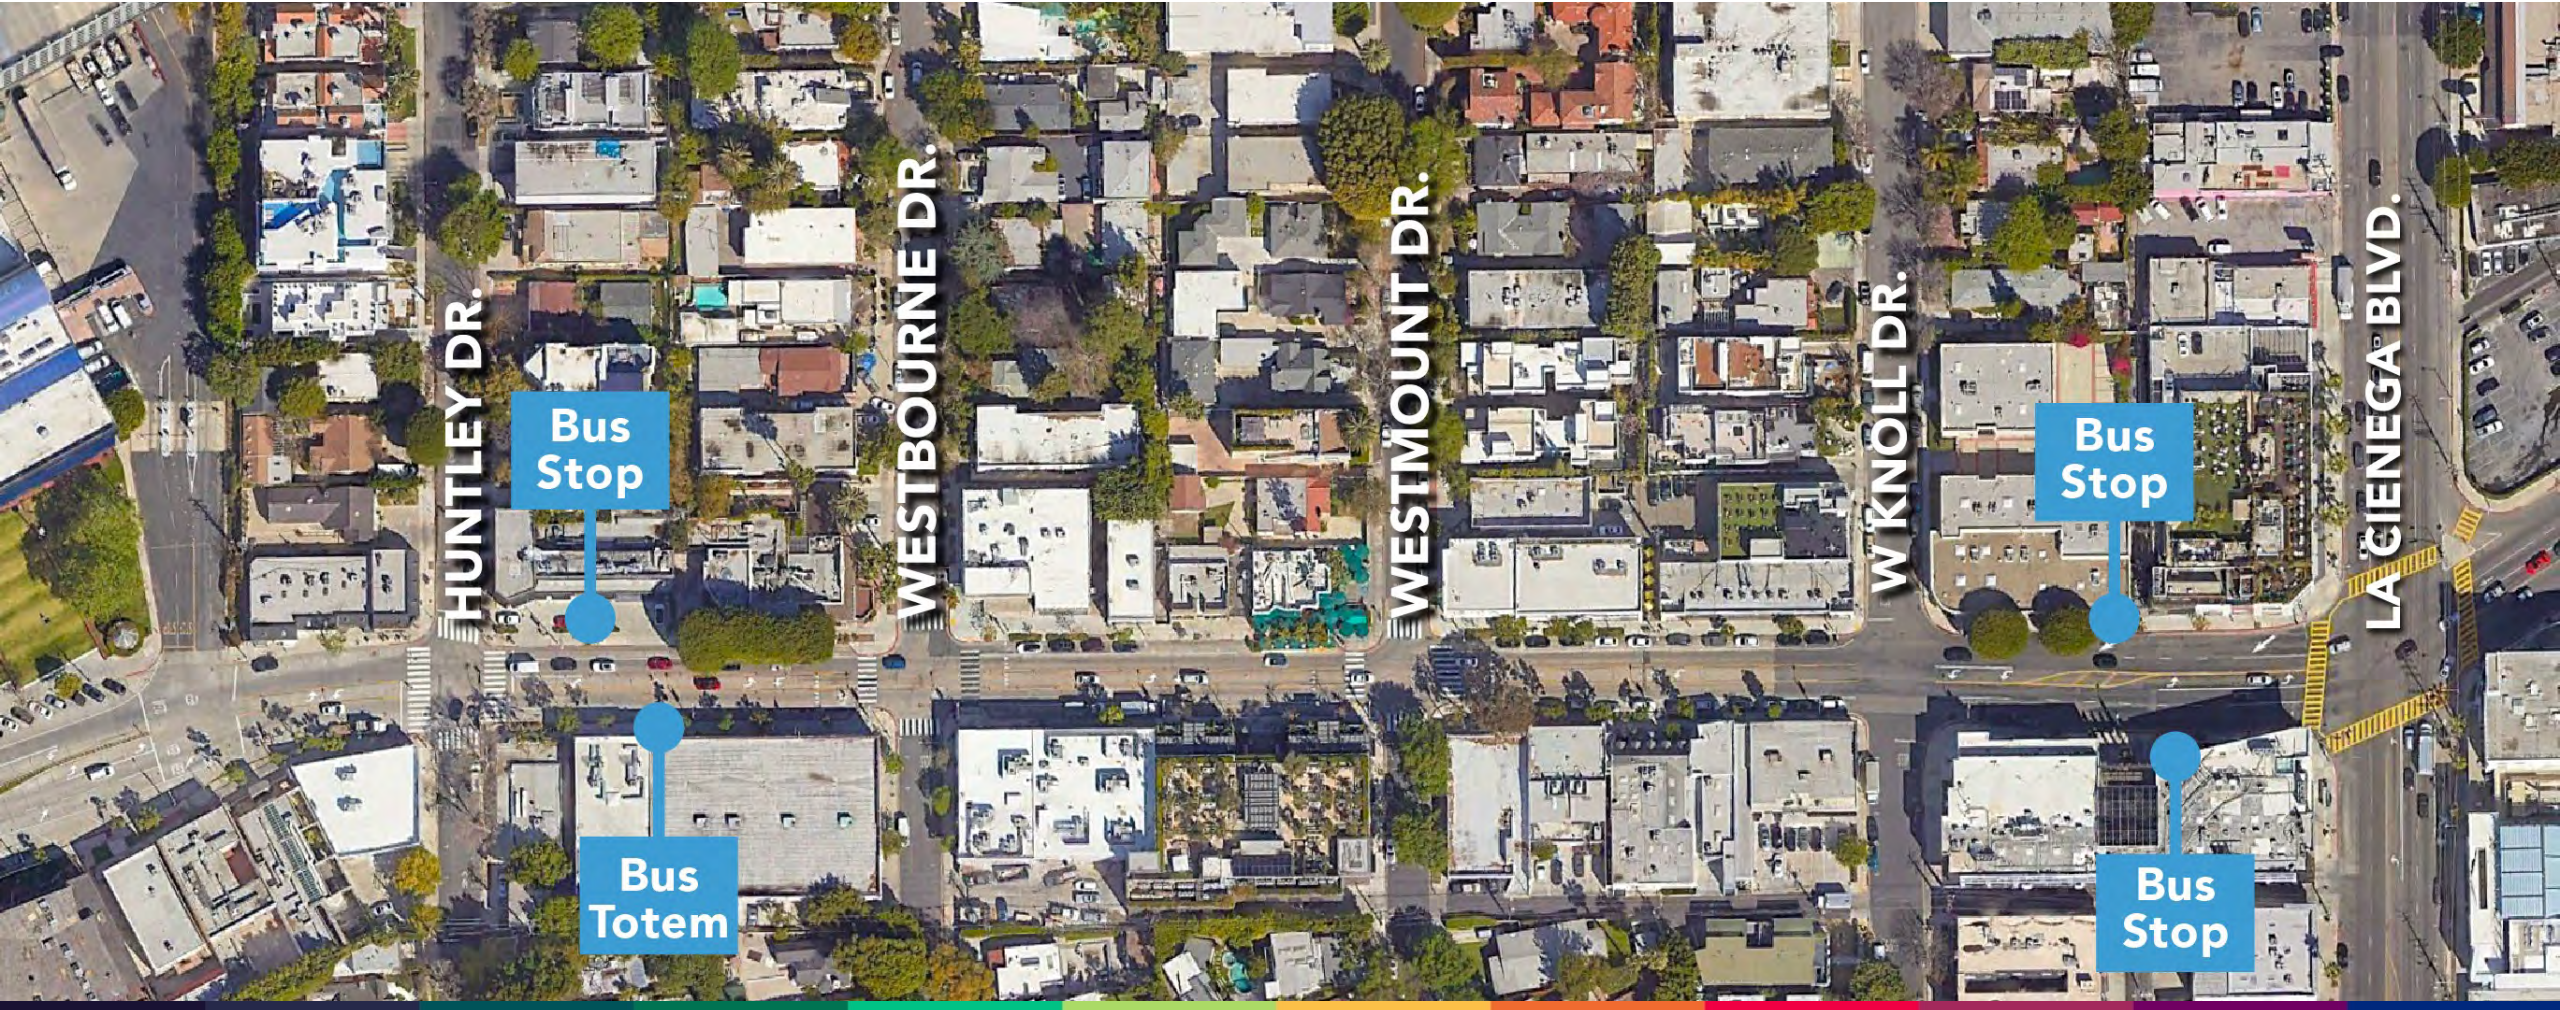

Lighted Crosswalks



Westbound Melrose at La Cienega



Final Construction Activities

- Irrigation system & testing
- Fiber optic cabling & splicing
- Landscape & lighting power
- Benches & bike racks
- Final asphalt grinding, paving & striping



75th ANNIVERSARY





JOIN OUR MAILING LIST

Email Us

WeHoDesignDistrictStreetscape
@bergcm.com



GIVE US FEEDBACK

Project Feedback Line

1 (800) 362-3996



VISIT OUR WEBSITE

Project Website

WeHoDesignDistrictStreetscape.com



QUESTIONS
