



City of West Hollywood
California 1984

WEHO | DESIGN DISTRICT STREETSCAPE

Construction Updates
August 31, 2023



Staged Schedule

Stage 1: May 9, 2022 – Nov 2022

Stage 3: Jul 2022 – Oct 6, 2022

Stage 5 (South): Oct 6, 2023 – Dec 30, 2023

Stage 5 (North): Jan 3, 2023 – April 3, 2023

Stage 4: April 3, 2023 – June 28, 2023

Stage 2: June 28, 2023 – Oct 2022



Current Activities

Sidewalk & Driveway Concrete Pours


- Pouring in stages over several days
- Concrete dates:
 - August 14 – 16, 2023
 - August 21 – 23, 2023
 - Sept. 5 – 6, 2023



Concrete Pours

Remaining Pours

- Decorative Band & Panels between Westbourne & Huntley: Sept. 5 & 6, 2023
- Norwich Gathering Space pours TBD

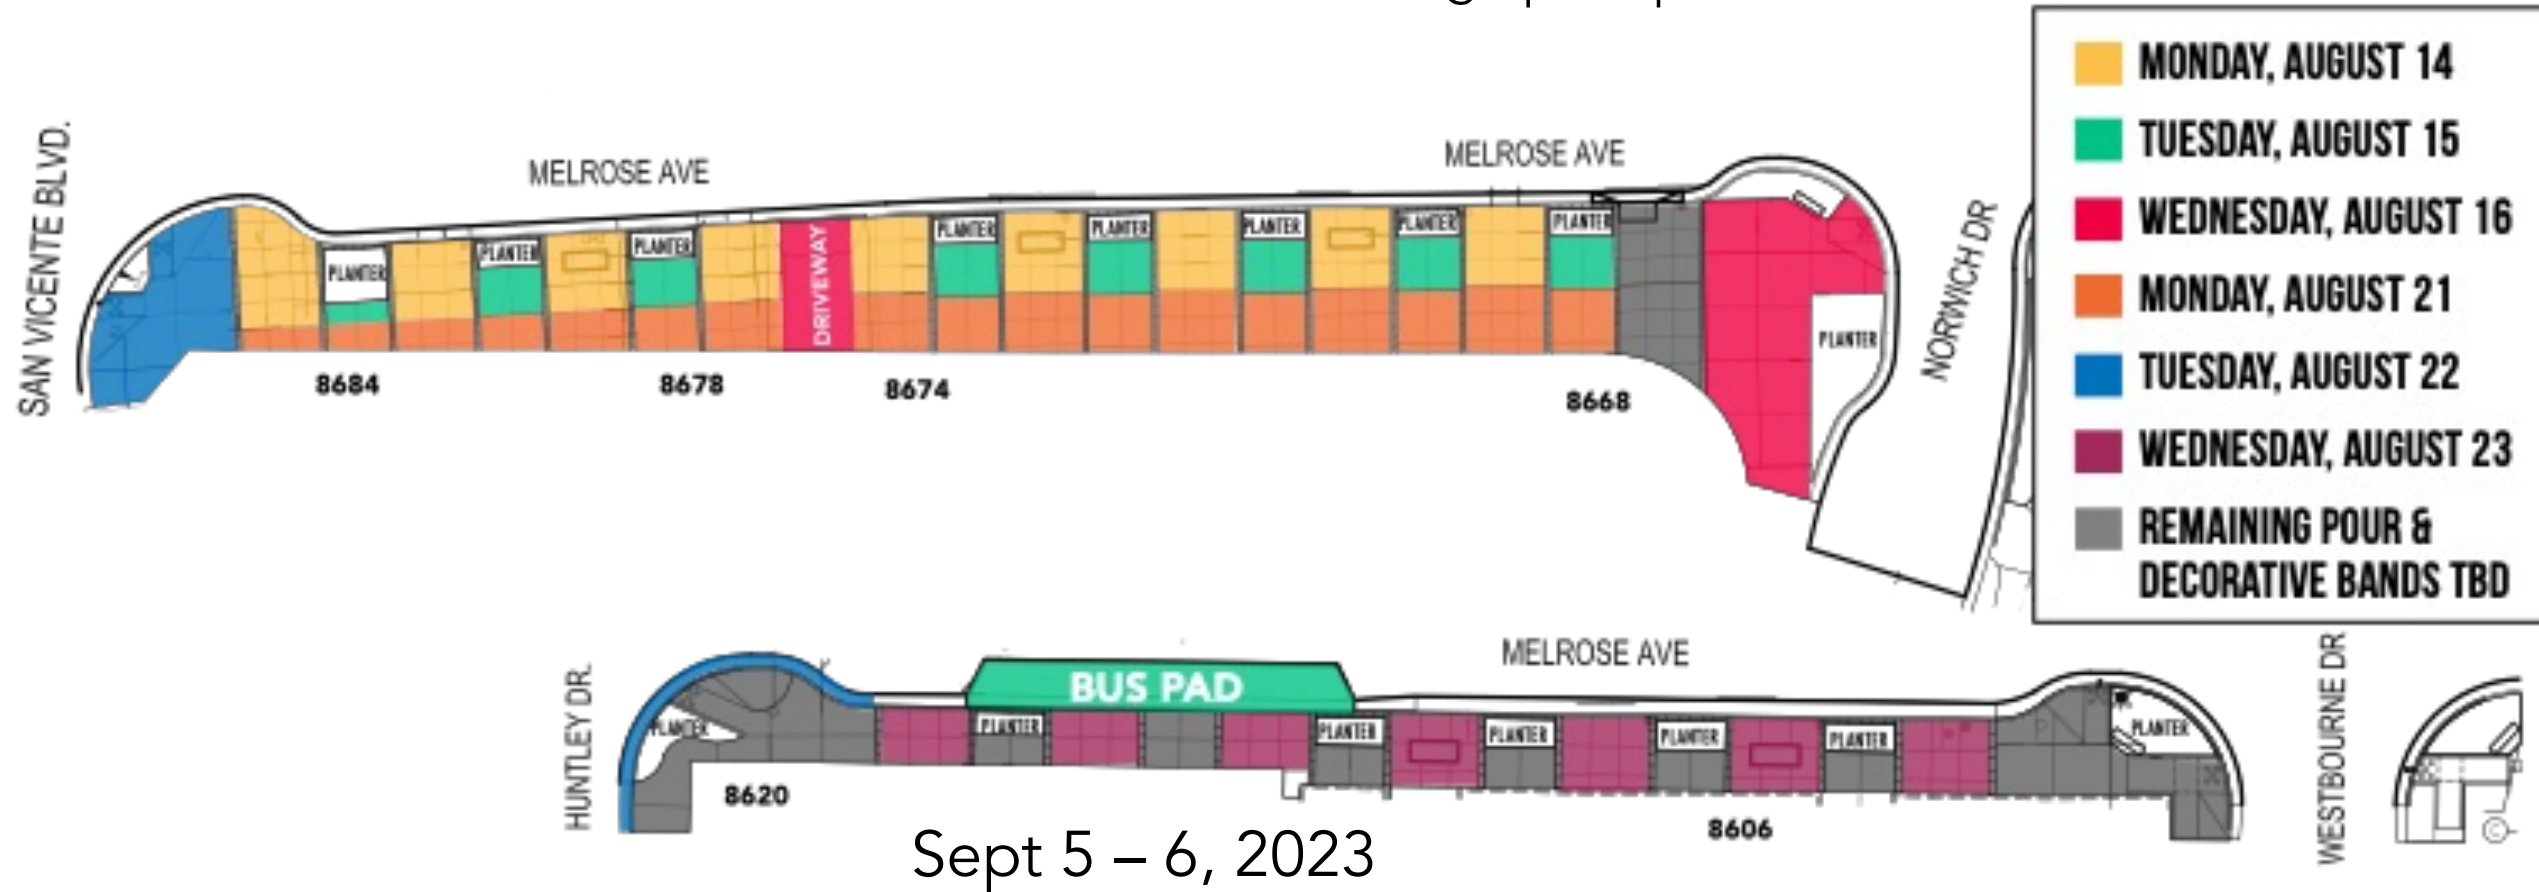

LADWP Mainline Project

Start date: August 23, 2023 (on Huntley)

Location:

- Huntley Drive from Melrose Ave to Sherwood
- West Knoll from Melrose Ave to Santa Monica Blvd.

Duration: Approximately 3 months

Schedule:

- Monday – Saturday
- 8AM – 4PM




Current Activities

Intersection Work:


- Day & night closures for approximately three days
- Intersections closed to north and south through traffic
- Lane obstructions on Melrose
- Daytime flaggers to guide pedestrians & traffic

Westbourne: September 6 – 8, 2023 (Wednesday – Friday)

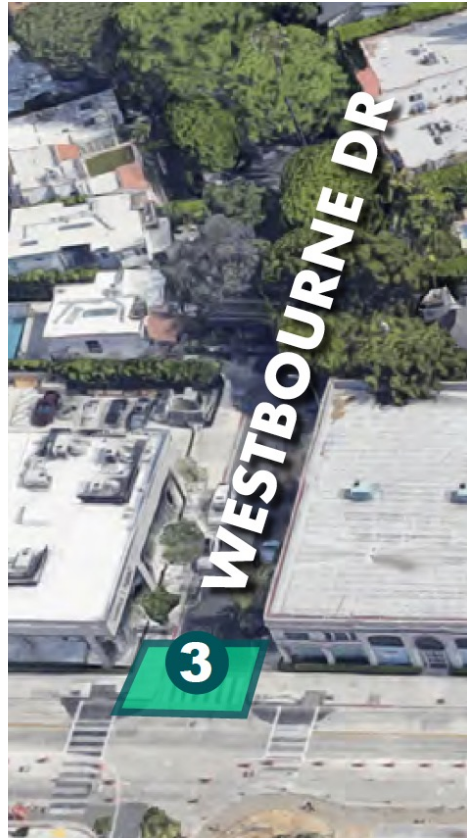

August 28 – 30, 2023
(Monday – Wednesday)

✓ DONE

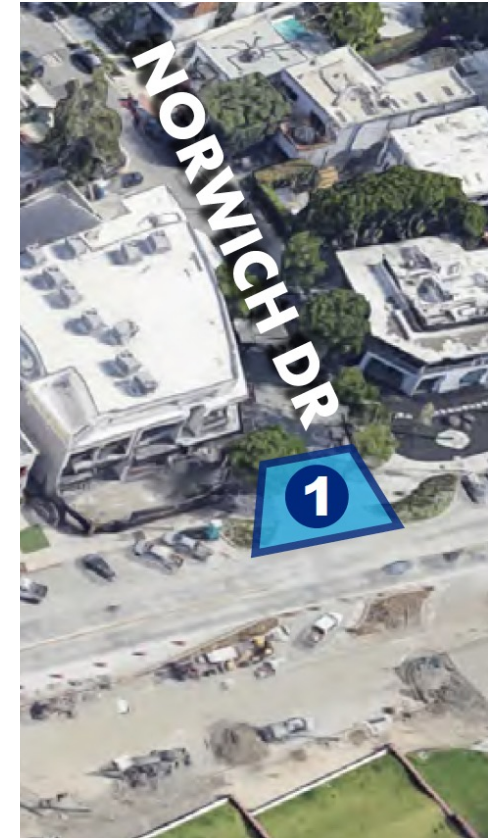

August 23 – 25, 2023
(Wednesday – Friday)

✓ DONE

Upcoming Activities

Storm Drain

- Install 2 new catch basins east and west of Norwich
- Date: TBD

Utilities

- AT&T relocate one cabinet in front of Hamilton Selway at San Vicente Blvd.
- Date: Next week, day TBD



Upcoming Activities

Sandblast Sidewalks

- Sidewalks will receive decorative sandblast treatment to add texture
- Bands and 5x5 panels will be sandblasted
- Business entrances will be sandblasted before opening
- Pedestrians will be detoured into street with delineated business access
- Sidewalks opened as work progresses
- Schedule TBD



Sandblast Texture Examples



Upcoming Activities

Uplifting & Deficient Sidewalk Replacement

- Remove and replace uplifted sidewalk
- Excavate 28 inches and replace with non-expansive soil
- Various location
- Schedule TBD – Late September




Norwich Gathering Space



Bus Shelters



Lighted Crosswalks

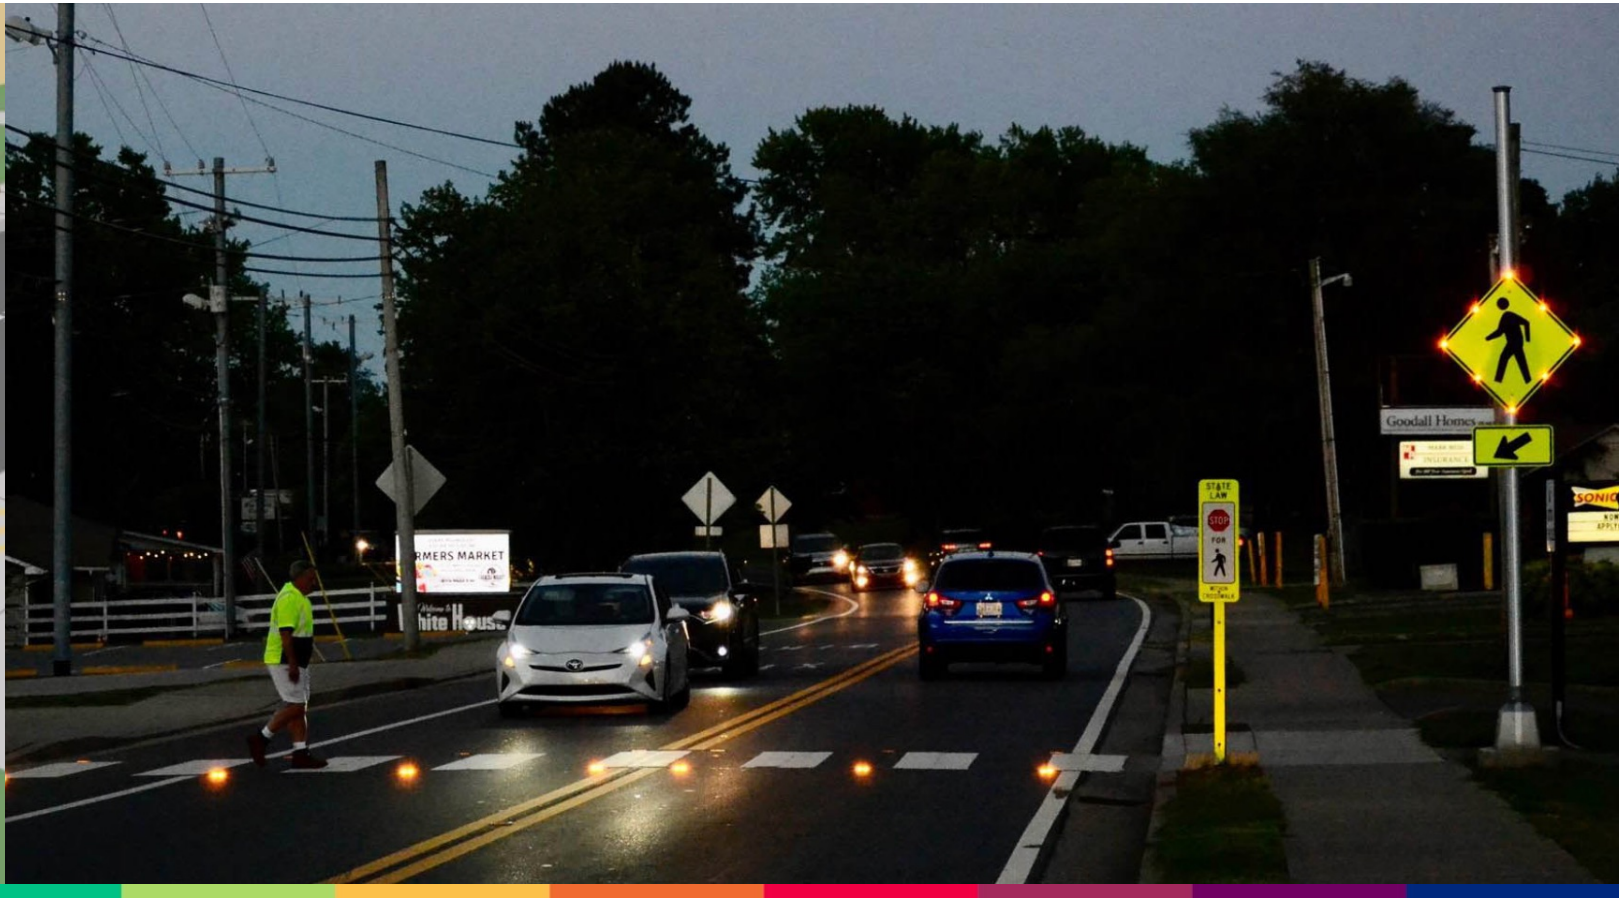

Final Construction Activities

- Irrigation system & testing: Done mid-Sept.
- Landscape planting: Begin Oct.
- Fiber optic cabling & splicing: Begin early-Oct.
- Benches & bike racks: Begin early Nov.
- Final asphalt grinding, paving, striping: Nov.



Final Construction Activities

Final Asphalt Grinding, Paving, Striping

- Three-day, double shift to expediate the work
 - Grinding: 9AM – 4PM
 - Paving: 9PM – 6AM (night work)
- Day work: Soft closures with flaggers (one-way traffic & local access only)
- Night work: Hard closures (road closed)



E/W Melrose at La Cienega



75th ANNIVERSARY





JOIN OUR MAILING LIST

Email Us

WeHoDesignDistrictStreetscape
@bergcm.com



GIVE US FEEDBACK

Project Feedback Line

1 (800) 362-3996



VISIT OUR WEBSITE

Project Website

WeHoDesignDistrictStreetscape.com

