



City of West Hollywood
California 1984

WEHO | DESIGN DISTRICT STREETSCAPE

Construction Updates
October 26, 2023



Staged Schedule

Stage 1: May 9, 2022 – Nov 2022

Stage 3: Jul 2022 – Oct 6, 2022

Stage 5 (South): Oct 6, 2023 – Dec 30, 2023

Stage 5 (North): Jan 3, 2023 – April 3, 2023

Stage 4: April 3, 2023 – June 28, 2023

Stage 2: June 28, 2023 – Nov 2023

Gathering Space: TBD

Final Activities in All Stages: Sept 2023 – Nov 2023



LADWP Mainline Project

Start date: August 23, 2023 (on Huntley)

Location:

- Huntley Drive from Melrose Ave to Sherwood – Began construction on Aug. 23. Currently performing tie-ins to all residences. Estimated to be complete in about 3 weeks (Thanksgiving).
- West Knoll from Melrose Ave to Santa Monica Blvd. – Began construction on Sept. 18. Anticipated to be complete in December.

Schedule:


- Monday – Saturday
- 8AM – 4PM



Current Activities

Remove and Replace Roadway

- Parking removals in the construction zone
- Traffic lane reductions
- Flagman-controlled one-way traffic in east and west directions
- Huntley intersection closure: Oct. 26, 2023
- Westbourne intersection closure: Oct. 27, 2023
- Pedestrian access will remain open

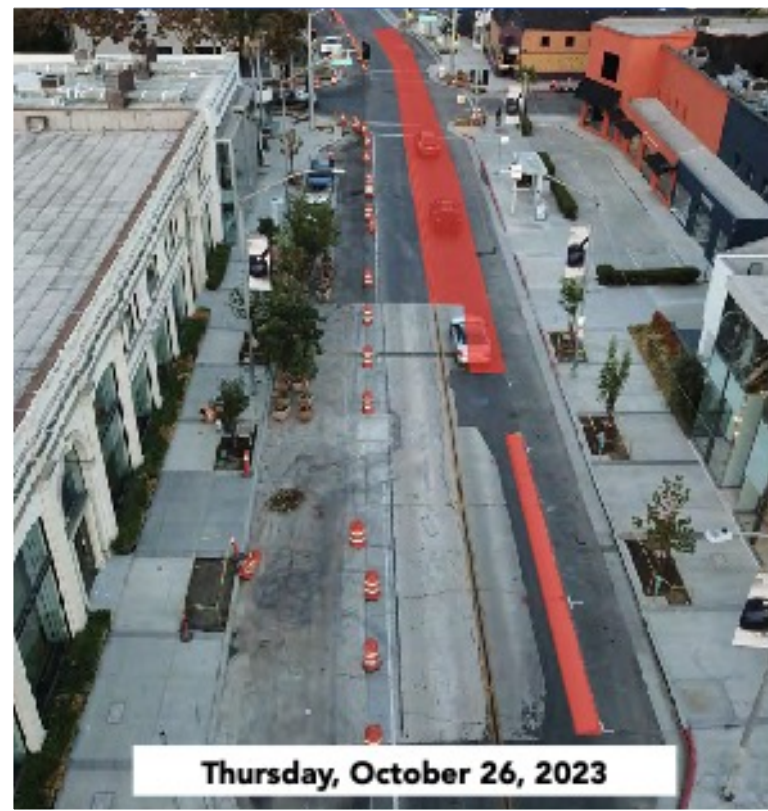

Current Activities

Sandblast Sidewalks

- Sidewalks will receive decorative sandblast treatment to add texture
- Bands and 5x5 panels will be sandblasted
- Pedestrians will be detoured into street with delineated business access
- Sidewalks opened as work progresses



Sidewalk Sandblast



		Approximate sandblast schedule
Oct. 05 – 13:	West Knoll to La Cienega (south)	
Oct. 16 – 20:	La Cienega to Croft (south)	
Oct. 26 – 30:	Croft to La Cienega (north)	
Oct. 23 – 25:	La Cienega to West Knoll (north – done!)	
TBD	West Knoll to Westmount (north)	
	... etc. working from east to west	



Final Construction Activities

- Irrigation system & testing: Late Oct. – completing Nov.
- Decorative sidewalk sandblasting: Ongoing
- Landscape planting: Ongoing
- Fiber optic cabling & splicing: Begin early Nov.
- Benches & bike racks: Begin early Nov.
- Final asphalt grinding, paving, striping: Nov. 1, 2, & 6



Final Construction Activities

Final Asphalt Grinding, Paving, Striping

- Three-day, double shift to expediate the work
 - Grinding: 8AM – 4PM
 - Paving: 9PM – 6AM (night work)
- Day work: Soft closures with flaggers (one-way traffic & local access only)
- Night work: Hard closures (road closed)





Croft Ave to La Cienega Blvd

**Day 1: Wed., Nov. 1, 2023;
8AM - 4PM**

What to expect:

- Roadway grinding with large machinery.
- Outside lane closures followed by inside lane closures.
- Flaggers to assist traffic flow.

**Night 1: Wed., Nov. 1, 2023;
9PM - Thurs., Nov. 2, 6AM**

What to expect:

- Roadway paving with large machinery.
- Outside lane closures followed by inside lane closures.
- Flaggers to assist traffic flow.

La Cienega Blvd to Westbourne Dr

**Day 2: Thur., Nov. 2, 2023;
8AM - 4PM**

What to expect:

- Roadway grinding with large machinery.
- Lane closures from La Cienega Blvd. to Westbourne Dr.
- Flaggers to assist with one-way traffic flow.

**Night 2: Thur., Nov. 2, 2023;
9PM - Fri., Nov. 3, 6AM**

What to expect:

- Roadway paving with large machinery.
- Road closed to thru-traffic from Westbourne Dr. to San Vicente Blvd.
- Hard closure (NO ACCESS) from La Cienega Blvd. to Westbourne Dr.

Westbourne Dr to San Vicente Blvd

**Day 3: Mon., November 6, 2023;
8AM - 4PM**

What to expect:

- Roadway grinding with large machinery.
- Lane closures from Westbourne Dr. to San Vicente Blvd.
- Flaggers to assist with one-way traffic flow.

**Night 3: Mon., Nov. 6, 2023;
9PM - Tues., Nov. 7, 6AM**

What to expect:

- Roadway paving with large machinery.
- Road closed to thru-traffic from La Cienega Blvd. to Westbourne Dr.
- Hard closure (NO ACCESS) from Westbourne Dr to San Vicente Blvd.

October 2023

September '23							November '23						
S	M	T	W	T	F	S	S	M	T	W	T	F	S
					1	2			1	2	3	4	
3	4	5	6	7	8	9	5	6	7	8	9	10	11
10	11	12	13	14	15	16	12	13	14	15	16	17	18
17	18	19	20	21	22	23	19	20	21	22	23	24	25
24	25	26	27	28	29	30	26	27	28	29	30		

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
22	23	24	25	26 R&R Asphalt Huntley Closure	27 R&R Asphalt Westbourne Closure	28
29	30 Landscaping Sandblasting Stage 5 North	31 Halloween No Work	1 Day/Night 1 Grind & Pave Croft to La Cienega	2 Day/Night 2 Grind & Pave La Cienega to Westbourne	3	4
5	6 Day/Night 3 Grind & Pave Westbourne to San Vicente	7	8	9	10	11
12	13	14	15	16	17	18

Norwich Gathering Space





JOIN OUR MAILING LIST

Email Us

WeHoDesignDistrictStreetscape
@bergcm.com



GIVE US FEEDBACK

Project Feedback Line

1 (800) 362-3996



VISIT OUR WEBSITE

Project Website

WeHoDesignDistrictStreetscape.com

