

City of West Hollywood
California 1984

WEHO | DESIGN DISTRICT STREETSCAPE

Construction Updates
November 9, 2023



Staged Schedule

Stage 1: May 9, 2022 – Nov 2022

Stage 3: Jul 2022 – Oct 6, 2022

Stage 5 (South): Oct 6, 2023 – Dec 30, 2023

Stage 5 (North): Jan 3, 2023 – April 3, 2023

Stage 4: April 3, 2023 – June 28, 2023

Stage 2: June 28, 2023 – Nov 2023

Gathering Space: TBD

Final Activities in All Stages: Sept 2023 – Nov 2023



LADWP Mainline Project

Start date: August 23, 2023 (on Huntley)

Location:

- Huntley Drive from Melrose Ave to Sherwood – Began construction on Aug. 23. Currently performing tie-ins to all residences. Estimated to be complete in about 2 weeks (Thanksgiving).
- West Knoll from Melrose Ave to Santa Monica Blvd. – Began construction on Sept. 18. Anticipated to be complete in December.

Schedule:

- Monday – Saturday
- 8AM – 4PM



Current Activities

Sandblast Sidewalks

- Sidewalks will receive decorative sandblast treatment to add texture
- Bands and 5x5 panels will be sandblasted
- Pedestrians will be detoured into street with delineated business access
- Sidewalks opened as work progresses



Sidewalk Sandblast

- Nov. 09 – 14: West Knoll to Westmount (north)
- Nov. 14 – 17: Westmount to Westbourne (north)
- Nov. 20 – 22: Westbourne to Huntley/Private Dr (north)
- Nov. 27 – 30: Remaining at PDC (north)

- Completed
- Ongoing
- Repairs

Approximate sandblast schedule



Current Activities

Utility Adjustments

- Adjusting manholes to grade after paving
- Started on Nov. 9, 2023
- Approximately 4 - 5 days of work

Landscape

- Shrub planting and placing mulch



Upcoming Activities

Final Striping


- Lane closures and intermittent parking obstructions for final roadway striping of lanes, parking tees, and crosswalks.

Crosswalks

- Lane closures for installation of in-roadway lighting at crosswalks.
- Anticipated completion mid-week: November 15, 2023



Lighted Crosswalks

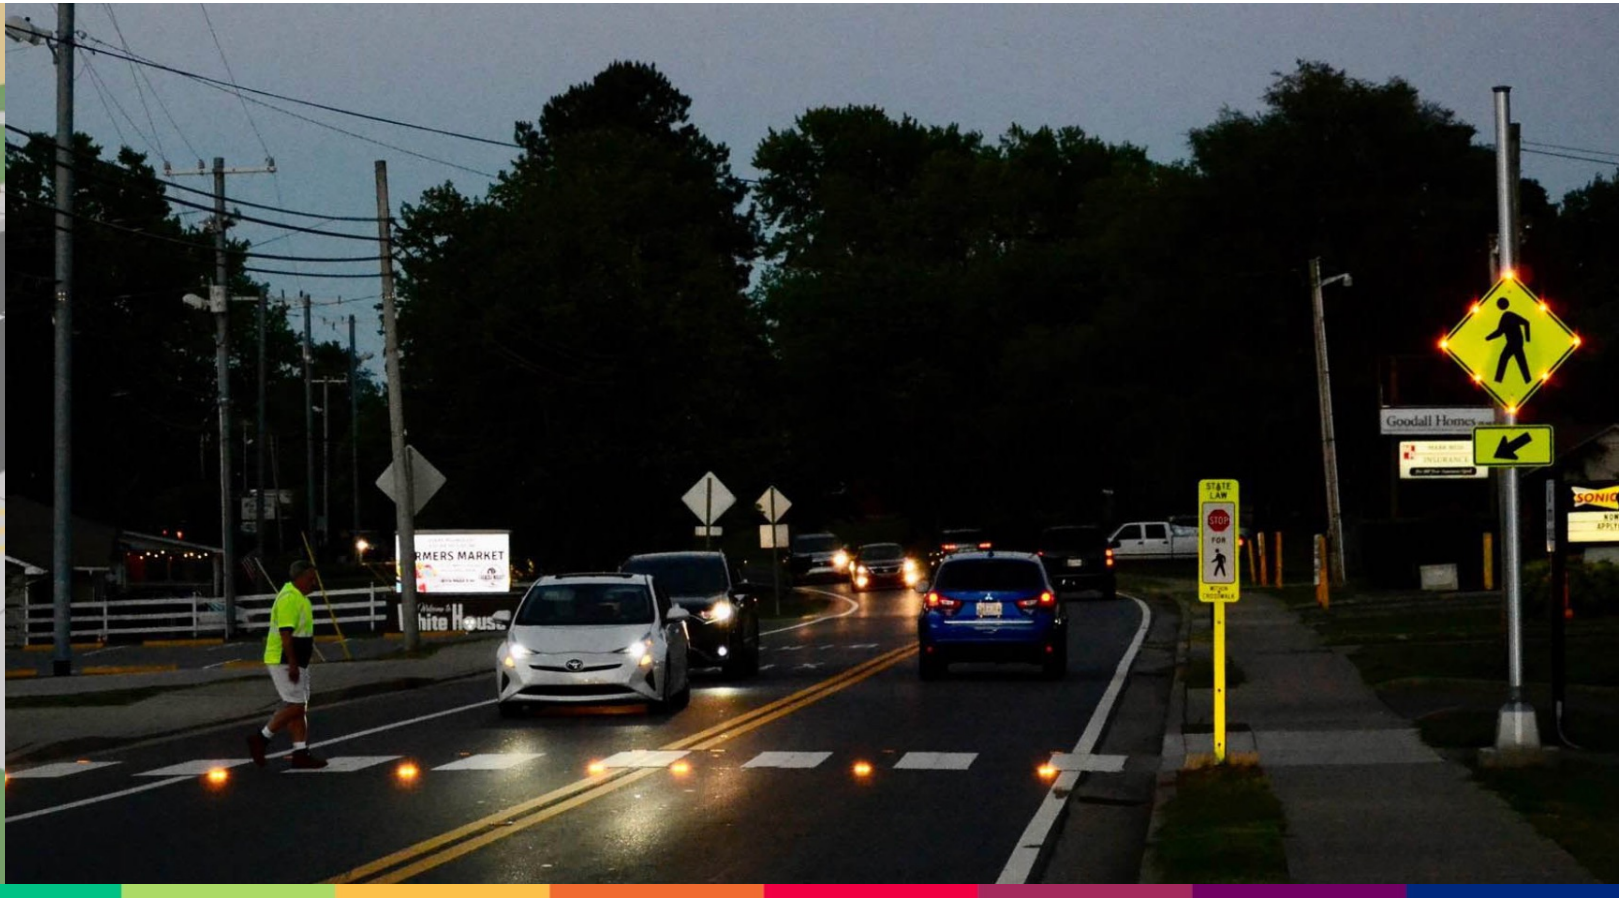

Upcoming Activities

Traffic Loops

- Lane closures on La Cienega for traffic signal loop detection installation.
- Monday & Tuesday, November 13 & 14, 2023

Hardscape Furnishing

- Installation of benches, bike racks, and trash receptacles – upcoming



November 2023

October '23							December '23						
S	M	T	W	T	F	S	S	M	T	W	T	F	S
1	2	3	4	5	6	7						1	2
8	9	10	11	12	13	14	3	4	5	6	7	8	9
15	16	17	18	19	20	21	10	11	12	13	14	15	16
22	23	24	25	26	27	28	17	18	19	20	21	22	23
29	30	31					24	25	26	27	28	29	30
							31						

Sunday	Monday	Tuesday	Wednesday	Thursday	Friday	Saturday
29	30	31 Halloween No Work	1 Day/Night 1 Grind & Pave Croft to La Cienega	2 Day/Night 2 Grind & Pave La Cienega to Westbourne	3	4
5	6 Day/Night 3 Grind & Pave Westbourne to San Vicente	7	8	9 Sandblasting West Knoll	10 Veterans Day Holiday No Work	11 PDC Event
12 PDC Event	13	14 Final roadway striping	15	16	17	18
	Sandblasting Sidewalks					
19	20	21	22	23 Thanksgiving No Work	24 Thanksgiving No Work	25
	Sandblasting Sidewalks					
26	27	28	29	30	1	2

Norwich Gathering Space





JOIN OUR MAILING LIST

Email Us

WeHoDesignDistrictStreetscape
@bergcm.com



GIVE US FEEDBACK

Project Feedback Line

1 (800) 362-3996



VISIT OUR WEBSITE

Project Website

WeHoDesignDistrictStreetscape.com

